

JOB NO.: TCS01216/21

**WSD Contract No.: 3/WSD/20 -
Reclaimed Water Supply to Sheung Shui and Fanling**

**MONTHLY ENVIRONMENTAL MONITORING & AUDIT
REPORT (NO.1) – DECEMBER 2021**

**PREPARED FOR
WATER SUPPLIES DEPARTMENT**

Quality Index

Date	Reference No.	Prepared By	Approved By
4 April 2022	TCS01216/21/600/R0019v3	 Martin Li Environmental Consultant	 TW Tam Environmental Team Leader

Version	Date	Description
1	7 January 2022	First Submission
2	13 January 2022	Amended against IEC's comments
3	4 April 2022	Information Updated



NATURE & TECHNOLOGIES (HK) LIMITED
科技環保(香港)有限公司

Unit D, 12/F, Ford Glory Plaza, Nos. 37-39 Wing Hong Street,
Cheung Sha Wan, Kowloon, Hong Kong
香港九龍長沙灣永康街 37-39 號福源廣場 12D
Tel 電話: (852) 2877 3122 Fax 傳真: (852) 2511 0922
Email 電郵 : enquiry@nt.com.hk Website 網址 : <http://www.nt.com.hk>

Date: 11th May 2022

Project Manager
Water Supplies Department
Immigration Tower, 7 Gloucester Road,
Wan Chai, Hong Kong
Attn: Mr. Freeman Kei

Dear Sir,


Agreement No. CE67/2017(WS)
Reclaimed Water Supply to Sheung Shi and Fanling – Investigation, Design and Construction
Independent Environmental Checker (IEC) Services for
Shek Wu Hui Water Reclamation Plant under Contract No. 3/WSD/20

Monthly EM&A Monitoring Report for December 2021 Version 3

We refer to the updated monthly EM&A Report for December 2021 for WSD Contract No.: 3/WSD/20 – Reclaimed Water Supply to Sheung Shui and Fanling certified by the Environmental Team Leader on 4th April 2022. Please note we have no adverse comments on the captioned submission. The captioned submission is hereby verified in accordance with the requirement stipulated in Condition 3.4 of Environmental Permit No. FEP-01/470/2013.

Should you have any query, please feel free to contact the undersigned at 2877 3122 or at 6113 2368 (vegawong@nt.com.hk).

Yours Sincerely,
For and on behalf of
Nature & Technologies (HK) Limited


Vega Wong
Independent Environmental Checker
c.c.

- ET Leader -- AUES (Attn: Mr. T.W. Tam) [by Email: twtam@fordbusiness.com]
- Resident Engineer – Binnies Hong Kong Limited (Attn: Mr. Chester Chan) [by Email: chancw@binnies.com]

EXECUTIVE SUMMARY

- ES.01 Water Supplies Department (WSD) is the Project Proponent and the Permit Holder of **Reclaimed Water Supply to Sheung Shui and Fanling** (hereinafter referred as “the Contract Works”), which is a Designated Project to be implemented under Further Environmental Permit number FEP-01/470/2013 (hereinafter referred as “the FEP-01/470/2013” or “the FEP”).
- ES.02 Action-United Environmental Services & Consulting (AUES) has been commissioned as the Environmental Team (hereinafter referred the “ET”) by the Main-Contractor (China Geo-Engineering Corporation) and the Resident Engineer (Binnies Hong Kong Limited) to perform relevant EM&A programmes for the Contract Works in accordance with the Updated EM&A Manual under the Environmental Impact Assessment Ordinance (EIAO).
- ES.03 In according with the Updated EM&A Manual stipulation and the location of Contract Works, only construction noise monitoring and waterbird of ecological monitoring are required during the construction phase of the Contract Works.
- ES.04 As part of the EM&A programme, baseline noise monitoring was conducted from **4 to 17 November 2021** by the ET in prior to commencement of the construction works under the Contract Works. Furthermore, baseline ecological of waterbirds monitoring along Ng Tung River, Sheung Yue River and Shek Sheung River was undertaken by Drainage Services Department (DSD) from **December 2017 to June 2019**. During the baseline noise monitoring period, no construction activities was carried out under the Project. However, other external influencing factors of significant concern was observed. Moreover, Baseline Monitoring Report (Report Ref. TCS01216/21/600/R0017v3) which summarized the key findings and the rationale behind determining a set of Action and Limit Levels (A/L Levels) from the baseline data has been verified by Independent Environmental Checker (IEC) and submitted to EPD endorsement on **24 November 2021** before construction activities of the Contract commencement.
- ES.06 As notified by China Geo-Engineering Corporation (hereinafter named as “the Main-Contractor”), construction works of the Contract Works commenced on 7 December 2021.
- ES.07 This is the **1st** monthly EM&A report presenting the monitoring results and inspection findings for the reporting period from **7 to 31 December 2021** (hereinafter ‘the Reporting Period’).

ENVIRONMENTAL MONITORING AND AUDIT ACTIVITIES

- ES.08 Environmental monitoring activities under the EM&A programme in the Reporting Period are summarized in the following table.

Environmental Aspect	Environmental Monitoring Parameters / Inspection	Total Occasions during Reporting Period
Construction Noise	L _{eq(30min)} Daytime	4
Ecology	Waterbirds	NA
Site Inspection Audit	ET, the Contractor and RE joint site Environmental Inspection	4

- ES.09 Since the Contract Works is a New Engineering Contract (NEC) under Works Bureau of Public Works Projects in Hong Kong, and the appointment of a qualified Ecologist is yet to be completed by the Main Contractor and the Resident Engineer to undertake the ecology of waterbirds monitoring. Therefore, no waterbirds survey was carried out in December 2021.
- ES.10 Although waterbirds survey was not carried out by this Contract in the Reporting Month, a waterbird survey with similar approach was conducted by nearby DSD Project Agreement No. SPW 12/2021 Shek Wu Hui Effluent Polishing Plant – Main Works under Further Environmental Permit No. FEP-02/474/2013. According to the waterbird survey result conducted by the abovementioned DSD Project, no significant decrease of waterbird was recorded in the Reporting Month and it is concluded that no disturbance to waterbird was caused by this Contract in the Reporting Month.

BREACH OF ACTION AND LIMIT (A/L) LEVELS

ES.11 In the Reporting Period, no construction noise was recorded exceedance the set performance criteria (i.e. 75dB(A)) and no noise complaint (i.e. Action Level) was received. No Notifications of Exceedances (NOEs) was issued to the Resident Engineer (RE), IEC and the Main Contractor. The statistics of environmental exceedance, NOE issued and investigation of exceedance are summarized in the following table.

Environmental Aspect	Monitoring Parameters	Action Level	Limit Level	Event & Action		
				NOE Issued	Investigation	Corrective Actions
Construction Noise	$L_{eq(30min)}$ Daytime	0	0	0	0	0

ENVIRONMENTAL COMPLAINT

ES.12 No public complaints as relative with environmental was received or registered by either the RE or CEDD or the Main Contractor in the Reporting Period.

NOTIFICATION OF SUMMONS AND SUCCESSFUL PROSECUTIONS

ES.13 No environmental summons or successful prosecutions were recorded in the Reporting Period.

REPORTING CHANGE

ES.14 As this is the first Monthly EM&A Report, no reporting changes were made in the Reporting Period.

SITE INSPECTION BY EXTERNAL PARTIES

ES.15 No site inspection was undertaken by EPD within the Reporting Period.

FUTURE KEY ISSUES

ES.16 Construction noise would be a key environmental issue during construction work of the Project. Noise mitigation measures such as using quiet plants should be implemented in accordance with the EM&A requirement.

ES.17 Moreover, the Contractor shall fully implement mitigation measures prevent dust emission and muddy water and other water pollutants via site surface water runoff get into the rivers.

TABLE OF CONTENTS

1.	INTRODUCTION	1
1.1	BACKGROUND	1
1.2	REPORT STRUCTURE	1
2.	PROJECT ORGANIZATION AND CONSTRUCTION PROGRESS	2
2.1	PROJECT ORGANIZATION	2
2.2	CONSTRUCTION PROGRESS	3
2.3	SUMMARY OF ENVIRONMENTAL SUBMISSIONS	3
3.	SUMMARY OF IMPACT MONITORING REQUIREMENTS	4
3.1	GENERAL	4
3.2	REQUIREMENT OF CONSTRUCTION NOISE MONITORING	4
3.3	LOCATION OF CONSTRUCTION NOISE IMPACT MONITORING	4
3.4	EVENT AND ACTION PLAN	4
3.5	NOISE MONITORING METHODOLOGY	5
3.6	MONITORING PROCEDURE	5
3.7	DATA MANAGEMENT AND DATA QA/QC CONTROL	5
3.8	REQUIREMENT OF WATERBIRDS ECOLOGICAL IMPACT MONITORING	6
3.9	EVENT ACTION PLAN	6
4.	CONSTRUCTION NOISE MONITORING	9
4.1	GENERAL	9
4.2	RESULTS OF NOISE MONITORING	9
5.	ECOLOGY WATERBIRD MONITORING	10
5.1	GENERAL	10
5.2	RESULTS OF WATERBIRDS SURVEY	10
6.	WASTE MANAGEMENT	11
6.1	GENERAL WASTE MANAGEMENT	11
6.2	RECORDS OF WASTE QUANTITIES	11
7.	SITE INSPECTION	12
7.1	REQUIREMENTS	12
7.2	FINDINGS / DEFICIENCIES DURING THE REPORTING MONTH	12
8.	ENVIRONMENTAL COMPLAINT AND NON-COMPLIANCE	13
8.1	ENVIRONMENTAL COMPLAINT, SUMMONS AND PROSECUTION	13
9.	IMPLEMENTATION STATUS OF MITIGATION MEASURES	14
9.1	GENERAL REQUIREMENTS	14
9.2	TENTATIVE CONSTRUCTION ACTIVITIES IN THE COMING MONTH	14
9.3	KEY ISSUES FOR THE COMING MONTH	14
10.	CONCLUSIONS AND RECOMMENDATIONS	15
10.1	CONCLUSIONS	15
10.2	RECOMMENDATIONS	15

LIST OF TABLES

TABLE 2-3-1	STATUS OF ENVIRONMENTAL LICENSES AND PERMITS
TABLE 3-4-1	ACTION AND LIMIT LEVELS FOR CONSTRUCTION NOISE
TABLE 3-5-1	EQUIPMENT OF NOISE IMPACT MONITORING
TABLE 3-8-1	MONITORING OF MEASURES TO MINIMIZE DISTURBANCE TO WATERBIRDS ON THE NG TUNG, SHEUNG YUE AND SHEK SHEUNG RIVERS
TABLE 3-8-2	ACTION AND LIMIT LEVELS FOR ECOLOGICAL (WATERBIRDS) OF CONSTRUCTION PHASE
TABLE 3-9-1	EVENT AND ACTION PLAN FOR CONSTRUCTION NOISE
TABLE 3-9-2	EVENT AND ACTION PLAN OF WATERBIRDS OF ECOLOGICAL
TABLE 4-2-1	SUMMARIES OF NOISE MONITORING RESULTS OF CP-KTN-NMS5
TABLE 5-1-1	REPRESENTATIVE WATERBIRDS
TABLE 6-2-1	SUMMARY OF QUANTITIES OF INERT C&D MATERIALS
TABLE 6-2-2	SUMMARY OF QUANTITIES OF C&D WASTES
TABLE 7-2-1	SITE OBSERVATIONS
TABLE 8-1-1	STATISTICAL SUMMARY OF ENVIRONMENTAL COMPLAINTS
TABLE 8-1-2	STATISTICAL SUMMARY OF ENVIRONMENTAL SUMMONS
TABLE 8-1-3	STATISTICAL SUMMARY OF ENVIRONMENTAL PROSECUTION
TABLE 9-1-1	ENVIRONMENTAL MITIGATION MEASURES

LIST OF APPENDICES

APPENDIX A	LOCATION OF SHEK WU HUI WATER RECLAMATION PLANT
APPENDIX B	PROJECT ORGANIZATION
APPENDIX C	MASTER CONSTRUCTION PROGRAM
APPENDIX D	DESIGNATED NOISE MONITORING STATION LOCATION
APPENDIX E	VALID CALIBRATION CERTIFICATES OF MONITORING EQUIPMENT
APPENDIX F	MONITORING SCHEDULE OF THE REPORTING MONTH AND COMING MONTH
APPENDIX G	DATABASE OF MONITORING RESULT
APPENDIX H	GRAPHICAL PLOTS FOR MONITORING RESULT
APPENDIX I	MONTHLY SUMMARY WASTE FLOW TABLE
APPENDIX J	IMPLEMENTATION SCHEDULE FOR ENVIRONMENTAL MITIGATION MEASURES (ISEMM)

1. INTRODUCTION

1.1 BACKGROUND

- 1.1.1 Water Supplies Department (WSD) is the Project Proponent of Utilization of Treated Sewage Effluent (TSE) from Shek Wu Hui Sewage Treatment Works. On 30th July 2021, China Geo-Engineering Corporation (hereinafter named as “the Main-Contractor”) was awarded WSD Contract Works 3/WSD/20 - Reclaimed Water Supply to Sheung Shui and Fanling (hereinafter referred as “the Contract Works”).
- 1.1.2 The major work of the Contract Works is to construct the Shek Wu Hui Water Reclamation Plant. Location of Shek Wu Hui Water Reclamation Plant is shown in [Appendix A](#). For the Contract Works, Shek Wu Hui Water Reclamation Plant construction is a Designated Project to be implemented under Further Environmental Permit number FEP-01/470/2013 (hereinafter referred as “the FEP-01/470/2013” or “the FEP”).
- 1.1.3 Pursuant to the FEP stipulation, the Main Contractor has commissioned Action-United Environmental Services & Consulting (hereinafter referred as “AUES”) as Environmental Team (hereinafter referred as “ET”) perform relevant EM&A programme and as well as the associated duties.
- 1.1.4 In according with the approved Updated EM&A Manual of CEDD Contract No. NDO 14/2018 – *Advance and First Stage Works of Kwu Tung North and Fanling North New Development Areas* (hereinafter referred as “the Updated EM&A Manual”), there are three rivers (Ng Tung River, Sheung Yue River and Shek Sheung River) and one noise sensitive receiver (CP-KTN-NMS5) located about 200m and 300m distances near working site boundaries of the Contract Works. Based on requirement of the Updated EM&A Manuals, construction noise and ecological waterbird monitoring therefore shall be required to carry out during the construction phase.
- 1.1.5 As part of EM&A program, baseline environmental monitoring required to be conducted prior to commencement of the construction works under the Project. Hence, baseline noise monitoring conducted by the ET was from **4 to 17 November 2021** at the designated location CP-KTN-NMS5. Furthermore, baseline ecological of waterbirds monitoring along Ng Tung River, Sheung Yue River and Shek Sheung River was undertaken by Drainage Services Department (DSD) from **December 2017 to June 2019**. During construction periods of the Contract Works, the findings of waterbirds ecological impact monitoring will be compared with DSD Contract “*SPW 08/2019 - Shek Wu Hui Effluent Polishing Plant - Main Works Stage 1*” the baseline survey results.
- 1.1.6 This is **1st** monthly EM&A report to presenting the monitoring results and inspection findings from **7 to 31 December 2021** of the Reporting Period.

1.2 REPORT STRUCTURE

- 1.2.1 The report was structured into the following sections:-

Section 1	<i>Introduction</i>
Section 2	<i>Project Organization and Construction Progress</i>
Section 3	<i>Summary of Impact Monitoring Requirements</i>
Section 4	<i>Construction Noise Monitoring</i>
Section 5	<i>Ecology Waterbirds Monitoring</i>
Section 6	<i>Waste Management</i>
Section 7	<i>Site Inspections</i>
Section 8	<i>Environmental Complaints and Non-Compliance</i>
Section 9	<i>Implementation Status of Mitigation Measures</i>
Section 10	<i>Conclusions and Recommendations</i>

2. PROJECT ORGANIZATION AND CONSTRUCTION PROGRESS

2.1 PROJECT ORGANIZATION

2.1.1 The project organization is shown in [Appendix B](#). The roles and responsibilities of the various parties involved in the EM&A process and the organizational structure of the organizations responsible for implementing the EM&A programme are outlined below.

Water Supplies Department (WSD)

2.1.2 WSD is the Project Proponent and the Permit Holder of the EP of the development of the Project and will assume overall responsibility for the project. An Independent Environmental Checker (IEC) shall be employed by WSD to audit the results of the EM&A works carried out by the ET.

Environmental Protection Department (EPD)

2.1.3 EPD is the statutory enforcement body for environmental protection matters in Hong Kong.

Engineer or Engineers Representative (ER)

2.1.4 The ER is responsible for overseeing the construction works and for ensuring that the works are undertaken by the Contractor in accordance with the specification and contract requirements. The duties and responsibilities of the ER with respect to EM&A are:

- Supervise the Contractor's activities and ensure that the requirements in the Contract Works Specific EM&A Manual are fully complied with;
- Inform the Contractor when action is required to reduce impacts in accordance with the Event and Action Plans;
- Employ an IEC to audit the results of the EM&A works carried out by the ET; and
- Comply with the agreed Event Contingency Plan in the event of any exceedance.

The Main Contractor

2.1.5 The Main Contractor is responsible perform construction works and for ensuring that the works are undertaken compliance with the specification and contract requirements. The duties and responsibilities of the Main Contractor with respect to EM&A are:

- Employ an Environmental Team (ET) to undertake monitoring, laboratory analysis and reporting of environmental monitoring and audit;
- Provide assistance to ET in carrying out monitoring and auditing;
- Submit proposals on mitigation measures in case of exceedances of Action and Limit levels in accordance with the Event and Action Plans;
- Implement measures to reduce impact where Action and Limit levels are exceeded; and
- Adhere to the agreed procedures for carrying out compliant investigation.

Environmental Team (ET)

2.1.6 The ET is responsible perform implementation EM&A programmes of the Contract Works as stipulated in the Updated EM&A Manual ensure the works are fully compliance with environmental regulations. The duties and responsibilities of the ET with respect to EM&A are:

- Set up all the required environmental monitoring stations;
- Monitor various environmental parameters as required in the EM&A Manual;
- Analyze the EM&A data and review the success of EM&A programme to cost effectively confirm the adequacy of mitigation measures implemented and the validity of the EIA predictions and to identify any adverse environmental impacts arising;
- Carry out site inspection to investigate and audit the Contractors' site practice, equipment and work methodologies with respect to pollution control and environmental mitigation, and take proactive actions to pre-empt problems;
- Audit and prepare audit reports on the environmental monitoring data and site environmental conditions;
- Report on the EM&A results to the IEC, Contractor, the ER and EPD or its delegated representative;
- Recommend suitable mitigation measures to the Contractor in the case of exceedance of

- Action and Limit levels in accordance with the Event and Action Plans;
- Undertake regular and ad-hoc on-site audits / inspections and report to the Contractor and the ER of any potential non-compliance; and
- Follow up and close out non-compliance actions.

Independent Environmental Checker (IEC)

- 2.1.7 The duties and responsibilities of IEC with respect to EM&A are:
- Review the EM&A works performed by the ET (at not less than monthly intervals);
 - Audit the monitoring activities and results (at not less than monthly intervals);
 - Report the audit results to the ER and EPD in parallel;
 - Review the EM&A reports (monthly summary reports) submitted by the ET;
 - Review the proposal on mitigation measures submitted by the Contractor in accordance with the Event and Action Plans;
 - Check the mitigation measures submitted by the Contractor in accordance with the Event and Action Plans;
 - Check the mitigation measures that have been recommended in the EIA and this Manual, and ensure they are properly implemented in a timely manner, when necessary;
 - Report the findings of site inspections and other environmental performance reviews to ER and EPD;
 - Coordinate the monitoring and auditing works for all the on-going contracts in the area in order to identify possible sources / causes of exceedances and recommend suitable remedial actions where appropriate; and
 - Coordinate the assessment and response to complaints / enquires from locals, green groups, district councils or the public at large.

2.2 CONSTRUCTION PROGRESS

- 2.2.1 In the Reporting Period, major construction activities of the Contract Works are listed in below. Moreover, a master construction program is enclosed in [Appendix C](#).
- Geotechnical investigation
 - Site formation works
 - Piling Work

2.3 SUMMARY OF ENVIRONMENTAL SUBMISSIONS

- 2.3.1 To according with the EP stipulation, the required documents has submitted to EPD for retention as listed below:
- Project Location Plans;
 - Updated Environmental Monitoring and Audit Manual of Project Specific (TCS01176/21/600/R0012v2); and
 - Baseline Monitoring Report (TCS01216/21/600/R0017v3) for the Project.
- 2.3.2 Summary of the relevant permits, licenses, and/or notifications on environmental protection for the Project is presented in [Table 2-3-1](#).

Table 2-3-1 Status of Environmental Licenses and Permits

Item	Description	Licence/Permit Status		
		Ref. no.	Effective Date	Expiry Date
1	Air Pollution Control (Construction Dust) Regulation	Notification was made on 3 Aug 2021	3 Aug 2021	Till the Contract ends
2	Waste Disposal Regulation – Billing Account for Disposal of Construction Waste	Account No.: 7041397	8 Aug 2021	Till the Contract ends
3	Chemical Waste Producer Registration	Application was made on 3 Aug 2021	3 Aug 2021	Till the Contract ends
4	Water Pollution Control Ordinance – Discharge Licence	Discharge Licence No.: WT00039707-2021	17 Nov 2021	30/11/2026
5	Construction Noise Permit	CNP No. GW-RN0857-21	24 Nov 2021	23 Feb 2022

3. SUMMARY OF IMPACT MONITORING REQUIREMENTS

3.1 GENERAL

3.1.1 According to the Updated EM&A Manual and the location of the Contract Works, only construction noise monitoring and waterbirds ecological of environmental monitoring are related the Contract Works during the construction phase. Details requirement of noise and waterbirds ecological impact monitoring are presented sub-sections as below.

3.2 REQUIREMENT OF CONSTRUCTION NOISE MONITORING

3.2.1 One set of $L_{eq(30min)}$ as 6 consecutive $L_{eq(5min)}$ between 0700-1900 hours on normal weekdays and once every week during course of works. If construction work necessary to carry out at other time periods, i.e. restricted time period (19:00 to 07:00 the next morning and whole day on public holidays) (hereinafter referred as “the restricted hours”), $L_{eq(5min)}$ measurement will be carried out in accordance with the CNP requirements. Supplementary information for data auditing, statistical results such as L_{10} and L_{90} shall also be obtained for reference.

3.2.2 Noise measurements shall not be made in fog, rain, wind with a steady speed exceeding 5m/s or wind with gusts exceeding 10m/s. The wind speed shall be checked with a portable wind speed meter capable of measuring the wind speed in m/s.

3.3 LOCATION OF CONSTRUCTION NOISE IMPACT MONITORING

3.3.1 According to the Updated EM&A Manual of CEDD Contract No. NDO 14/2018 - *Advance and First Stage Works of Kwu Tung North and Fanling North New Development Areas*, four noise sensitive receivers are designated on Fanling North New Development Areas for construction noise monitoring.

3.3.2 According to the geographic location of proposed Shek Wu Hui Water Reclamation Plant and all the recommended designated construction noise monitoring stations, only the designated noise monitoring station CP-KTN-NMS5 (prior named “CP-NMS7”) shown in [Appendix D](#), is located near the proposed Shek Wu Hui Water Reclamation Plant within 300m (distance about 110m). Therefore, the designated noise monitoring station CP-KTN-NMS5 is recommended for the Contract Works to undertake construction noise monitoring. If the recommended noise monitoring location CP-KTN-NMS5 not available, the ET shall propose alternative monitoring locations/additional monitoring locations and seek approval from the Supervisor of the proposal. When alternative/new monitoring location is proposed, the monitoring location shall be chosen based on the following criteria:

- (i) at locations close to the major site activities which are likely to have noise impacts;
- (ii) close to the noise sensitive receivers; and
- (iii) for monitoring locations located in the vicinity of the sensitive receivers, care shall be taken to cause minimal disturbance to the occupants during monitoring.

3.3.3 The construction noise monitoring station shall normally be at a point 1 m from the exterior of the sensitive receivers building façade and be a position 1.2m above the ground. If there is problem with access to the normal monitoring position, an alternative position may be chosen, and a correction to the measurements shall be made to the free field measurements. The ET shall agree with the Supervisor on the monitoring station that is chosen for impact monitoring.

3.4 EVENT AND ACTION PLAN

3.4.1 The Action and Limit levels for construction noise are defined in *Table 3-4-1*. Should non-compliance of the criteria occur, action in accordance with the Action Plan which shown in Section 4 of this report, shall be carried out.

Table 3-4-1 Action and Limit Levels for Construction Noise

Monitoring Location	Action Level	Limit Level in dB(A)
	Time Period: 0700-1900 hours on normal weekdays	
CP-KTN-NMS5	When one or more documented complaints are received	75 dB(A) ^{Note 1}

Note 1: If works are to be carried out during restricted hours, the conditions stipulated in the construction noise permit issued by the NCA have to be followed.

3.5 NOISE MONITORING METHODOLOGY

Monitoring Equipment

3.5.1 Sound level meter in compliance with the International Electrotechnical Commission Publications 651: 1979 (Type 1) and 804: 1985 (Type 1) specifications was used for carrying out the noise monitoring. Noise equipment used for impact monitoring is listed in **Table 3-5-1**.

Table 3-5-1 Equipment of Noise Impact Monitoring

Equipment	Model
Integrating Sound Level Meter	Rion NL – 52 / B&K 2238
Calibrator	Rion NC – 74 / B&K 4231

Remark: Sound level meter IEC 60651:1979 (Type 1) was replaced by 60672 (Type 1) in 2002 (Ref: <https://webstore.iec.ch/publication/17086>)

3.5.2 The sound level meter and calibrator are calibrated and certified by a laboratory accredited under HOKLAS or any other international accreditation scheme at yearly basis. The valid calibration certificates of the monitoring equipment are shown in **Appendix E**.

3.6 MONITORING PROCEDURE

3.6.1 All noise measurements were performed with the meter set to FAST response and on the A-weighted equivalent continuous sound pressure level (Leq). Leq_(30min) in six consecutive Leq_(5min) measurements was used as the monitoring parameter for the time period between 07:00-19:00 hours during the baseline monitoring.

3.6.2 In general, the sound level meter would be mounted on a tripod at a height of 1.2 m and placed at the assessment point and oriented such that the microphone was pointed to the site with the microphone facing perpendicular to the line of sight. The windshield would be fitted for all measurement. Where a measurement was to be carried out at a building, the assessment point would normally be at a position 1 m from the exterior of the building façade. Where a measurement was to be made for noise being received at a place other than a building, the assessment point would be at a position 1.2 m above the ground in a free-field situation, i.e. at least 3.5 m away from reflective surfaces such as adjacent buildings or walls.

3.6.3 Immediately prior to and following each noise measurement the accuracy of the sound level meter was checked using an acoustic calibrator generating a known sound pressure level at a known frequency. Measurements would be accepted as valid only if the calibration level from before and after the noise measurement agrees to within 1.0 dB.

3.6.4 Noise measurements would not be made in fog, rain, wind with a steady speed exceeding 5m/s or wind with gusts exceeding 10m/s. The wind speed would be checked with a portable wind speed meter capable of measuring the wind speed in m/s.

3.7 DATA MANAGEMENT AND DATA QA/QC CONTROL

3.7.1 The monitoring data recorded in the equipment would be downloaded directly from the equipment at each monitoring day. The downloaded monitoring data would input into a computerized database properly maintained and handled by the ET's in-house data recording and management system.

3.8 REQUIREMENT OF WATERBIRDS ECOLOGICAL IMPACT MONITORING

3.8.1 Where development under the NDAs project is undertaken within 200m (the maximum distance at which it is predicted there may be some disturbance, and hence a reduction in numbers, of large waterbirds) of the Ng Tung, Sheung Yue and Shek Sheung Rivers and Long Valley the monitoring protocol detailed in the updated EM&A Manual Table 12.1 should be followed. A transect should be undertaken throughout the sections of the rivers where NDA construction activities are proposed; as the sensitive receivers (large waterbirds) are easily visible, the transect route needs only follow one bank of the rivers. The transect route should remain the same during the different phases in order to ensure that data are comparable. Monitoring of large waterbirds should be conducted in pre-construction, construction and operational phases of the concerned development.

3.8.2 The proposed Shek Wu Hui Water Reclamation Plant location is located less than 200m to Ng Tung River, Sheung Yue River and Shek Sheung River, waterbirds ecological monitoring included pre-construction (i.e. baseline), construction (i.e. impact) and post-construction (i.e. operating) should be requires. The detailed monitoring protocol is listed in *Table 3-8-1*.

Table 3-8-1 Monitoring of Measures to Minimize Disturbance to Waterbirds on the Ng Tung, Sheung Yue and Shek Sheung Rivers

Phase	Methodology
Pre-construction (baseline)	Weekly transect at both high and low tides to identify and enumerate all bird species utilising the river channels for 12 months prior to the commencement of construction.
Construction	Weekly transect at both high and low tides to identify and enumerate all bird species utilising the river channels and identify any sources of actual or potential disturbance to birds due to construction activities throughout the construction period.
Post-construction	Weekly transect at both high and low tides to identify and enumerate all bird species utilising the river channels and identify any sources of actual or potential disturbance to birds due to operational activities for 12 months following the completion of the construction period.

3.8.3 Waterbirds ecological baseline monitoring at Ng Tung River, Sheung Yue River and Shek Sheung River was conducted by DSD between *December 2017* and *June 2019* (total 19 months baseline monitoring), in compliance with the Updated EM&A Manual. Thus, the action and limit levels and responses to evidence of disturbance to waterbirds using in Ng Tung, Sheung Yue and Shek Sheung Rivers will be made reference during construction phase of the Project.

3.8.4 Measures to respond to decrease in numbers of large waterbirds using the river channels and action and limit levels to trigger these measures are detailed in *Table 3-8-2*.

Table 3-8-2 Action and Limit Levels for Ecological (Waterbirds) of Construction Phase

Action Level	Limit Level
Decline in numbers of all waterbird species relative to numbers during Baseline Monitoring such that the Action Level response is triggered.	Decline in numbers of all waterbird species relative to numbers during Baseline Monitoring such that the Limit Level response is triggered.
Decline in numbers of any one waterbird species occurring in significant numbers (*) during Baseline Monitoring such that the Action Level response is triggered.	Decline in numbers of any one waterbird species occurring in significant numbers (*) during Baseline Monitoring such that the Limit Level response is triggered.

(*) *Waterbird numbers refer to combined numbers using the channels*

3.9 EVENT ACTION PLAN

Noise

3.9.1 Should non-compliance of the construction noise criteria occur, action in accordance with the Action Plan in **Table 3-9-1** shall be carried out.

Table 3-9-1 Event and Action Plan for Construction Noise

Event	Action			
	ET	IEC	ER	Contractor
Action Level Exceedance	<ol style="list-style-type: none"> 1. Notify the IEC, ER and Contractor; 2. Carry out investigation; 3. Report the results of investigation to the IEC, ER and Contractor; 4. Discuss with the Contractor and formulate remedial measures; 5. Increase monitoring frequency to check mitigation effectiveness. 	<ol style="list-style-type: none"> 1. Review the monitoring data submitted by the ET; 2. Review the construction methods and proposed remedial measures by the Contractor, and advise the ET and ER if the proposed remedial measures would be sufficient; 3. Supervise the implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify the Contractor; 3. Require the Contractor to propose remedial measures for the analyzed noise problem; 4. Ensure remedial measures are properly implemented. 	<ol style="list-style-type: none"> 1. Submit noise mitigation proposals to the ER and IEC and copy to the ET; 2. Implement noise mitigation proposals.
Limit Level Exceedance	<ol style="list-style-type: none"> 1. Identify sources. 2. Inform IEC, ER, EPD and Contractor; 3. Repeat measurements to confirm findings; 4. Increase the monitoring frequency; 5. Carry out analysis of the Contractor's working procedures with the ER and Contractor to determine possible mitigations to be implemented; 6. Inform IEC, ER, EPD and Contractor the causes and actions taken for the exceedances; 7. Assess the effectiveness of the Contractor's remedial action with the ER and keep the IEC informed of the results; 8. If exceedance stops, cease additional monitoring. 	<ol style="list-style-type: none"> 1. Discuss amongst the ER, ET and Contractor on the potential remedial actions; 2. Review the Contractor's remedial action whenever necessary to assure their effectiveness and advise the ER accordingly; 3. Supervise the implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of exceedance in writing; 2. Notify the Contractor. 3. Require the Contractor to propose remedial measures for the analyzed noise problems; 4. Ensure remedial measures are properly implemented; 5. If exceedance continues, consider what portion of work is responsible and instruct the Contractor to stop that portion of works until the exceedance is abated. 	<ol style="list-style-type: none"> 1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial action to the ER and IEC and copy to the ET within 3 working days of notification; 3. Implement the agreed proposals; 4. Resubmit proposals if problems still not under control; stop the relevant portion of works as determined by the ER until the exceedance is abated.

Waterbird of Ecological

3.9.2 Should any exceedance encountered during construction phase, action in accordance with the Action Plan listed in **Table 3-9-2** shall be carried out.

Table 3-9-2 Event and Action Plan of Waterbirds of Ecological

Exceedance	Responses
Action Level	<ul style="list-style-type: none">Investigate cause and if cause identified as related to the Project, instigate remedial action to remove or reduce the source of disturbance.
Limit Level	<ul style="list-style-type: none">Investigate cause and if caused identified related to the Project, instigate remedial action.Review and adjust project's management measures to improve conditions for affected species.

4. CONSTRUCTION NOISE MONITORING

4.1 GENERAL

4.1.1 The noise monitoring schedule is presented in *Appendix F* and the monitoring results are presented in the following sections.

4.2 RESULTS OF NOISE MONITORING

4.2.1 In the Reporting Period, a total of **4** occasions noise monitoring were carried out at the designated location CP-KTN-NMS5. The sound level meter was set in free-field situation, and therefore, façade correction (+3dB) is added according to acoustical principles and EPD guidelines. The noise monitoring results at the designated locations are summarized in *Tables 4-2-1*. The detailed noise monitoring data is presented in *Appendix G* and the relevant graphical plot shown in *Appendix H*.

Table 4-2-1 Summaries of Noise Monitoring Results of CP-KTN-NMS5

Date	Start Time	L _{Aeq30min} (dB(A))
10-Dec-21	09:10	66.5
15-Dec-21	09:18	57.7
22-Dec-21	10:33	59.3
29-Dec-21	10:06	56.5
Limit Level		75 dB(A)

Note: façade correction +3dB has added according to acoustical principles and EPD guidelines

4.2.2 During construction noise monitoring, no rain was encountered and wind speed is below 5m/s and gusts not exceeding 10m/s. Piling underway for the Contract Works was observed during noise monitoring.

4.2.3 As shown in *Table 4-2-1*, the noise level measured at the designated monitoring location was below 75dB(A). Furthermore, there were no noise complaints (Action Level exceedance) received by the RE, Contractor, WSD or EPD in the Reporting Period. Therefore, no Action or Limit Level exceedance was triggered and no corrective action was therefore required.

4.2.4 During the reporting period, no construction work was carried out during restricted hours.

5. ECOLOGY WATERBIRD MONITORING

5.1 GENERAL

- 5.1.1 Ecological monitoring for waterbirds shall be performed as transects and point count surveys along Ng Tung River, Sheung Yue River and Shek Sheung River in accordance with general surveying practices.
- 5.1.2 The surveying shall be undertaken by a qualified ecologist and he/she shall be a member of the ET. Throughout the construction period, weekly transect shall be conducted at both high and low tides to identify and enumerate all bird species utilising the river channels and identify any sources of actual or potential disturbance to birds due to construction activities.
- 5.1.3 Since occurrence of waterbirds has distinctive seasonal pattern, the construction phase data for all waterbirds and representative waterbirds shall be compared with the baseline data for the respective month and season. The representatives of waterbirds are listed in **Table 5-1-1**.

Table 5-1-1 Representative Waterbirds

Species Name	Common Name	Chinese Name
Egretta garzetta	Little Egret	小白鷺
Ardea alba	Great Egret	大白鷺
Ardea cinerea	Grey Heron	蒼鷺
Ardeola bacchus	Chinese Pond Heron	池鷺
Bubulcus coromandus	Eastern Cattle Egret	牛背鷺
Phalacrocorax carbo	Great Cormorant	普通鸕鶿

5.2 RESULTS OF WATERBIRDS SURVEY

- 5.2.1 Since the Contract Works is a New Engineering Contract (NEC) under Works Bureau of Public Works Projects in Hong Kong, and the appointment of a qualified Ecologist is yet to be completed by the Main Contractor and the Resident Engineer to undertake the ecology of waterbirds monitoring. Therefore, no waterbirds survey was carried out in the Reporting Month.
- 5.2.2 Although waterbirds survey was not carried out by this Contract in the Reporting Month, a waterbird survey with similar approach was conducted by nearby DSD Project Agreement No. SPW 12/2021 Shek Wu Hui Effluent Polishing Plant – Main Works under Further Environmental Permit No. FEP-02/474/2013. According to the waterbird survey result conducted by the abovementioned DSD Project, no significant decrease of waterbird was recorded in the Reporting Month.
- 5.2.3 In addition, the construction activities of Contract Works is mainly piling work in the Reporting Month. The recorded construction noise levels are well below 75dB(A) and are similar to background noise of baseline monitoring. It is considered that the construction activities of the Contract Works should unlikely cause disturbance waterbird.

6. WASTE MANAGEMENT

6.1 GENERAL WASTE MANAGEMENT

6.1.1 Waste management was carried out by an on-site Environmental Officer or an Environmental Supervisor from time to time.

6.2 RECORDS OF WASTE QUANTITIES

6.2.1 All types of waste arising from the construction work are classified into the following:

- Construction & Demolition (C&D) Material;
- Chemical Waste;
- General Refuse; and
- Excavated Soil.

6.2.2 The quantities of waste for disposal in this Reporting Period are summarized in *Tables 6-2-1* and *6-2-2* and the Monthly Summary Waste Flow Table is shown in *Appendix I*. Whenever possible, materials were reused on-site as far as practicable.

Table 6-2-1 Summary of Quantities of Inert C&D Materials

Type of Waste	Quantity	Disposal Location
C&D Materials (Inert) (in '000m ³)	0.244	-
Reused in this Contract (Inert) (in '000 m ³)	0	-
Reused in other Contracts/ Projects (Inert) (in '000 m ³)	0	-
Disposal as Public Fill (Inert) (in '000 m ³)	0.244	TM38

Table 6-2-2 Summary of Quantities of C&D Wastes

Type of Waste	Quantity	Disposal Location
Recycled Metal ('000kg)	0	-
Recycled Paper / Cardboard Packing ('000kg)	0	-
Recycled Plastic ('000kg)	0	-
Chemical Wastes ('000kg)	0	-
General Refuses ('000m ³)	0	-

7. SITE INSPECTION

7.1 REQUIREMENTS

7.1.1 According to the approved Updated EM&A Manual, the environmental site inspection shall be formulation by ET Leader. Weekly environmental site inspections should carry out to confirm the environmental performance.

7.2 FINDINGS / DEFICIENCIES DURING THE REPORTING MONTH

7.2.1 In the Reporting Month, weekly regular site inspection by the RE, the Main Contractor and ET was carried out on **9, 16, 23 and 29 December 2021** to evaluate site environmental performance of the Contract Works. During the four occasion site inspections, no non-compliance was noted.

7.2.2 The findings/deficiencies of the Contract Works observed that during the weekly site inspection are listed in *Table 7-2-1*.

Table 7-2-1 Site Observations

Date	Findings / Deficiencies	Follow-Up Status
9 Dec 2021	No adverse environmental issue was observed during site inspection.	Nil
16 Dec 2021	<ul style="list-style-type: none"> One generator used near site entrance was observed the NRMM label damage, the Main Contractor was advised to replace the broken NRMM label. An oil drum located near site office was observed without drip tray. To avoid potential oil leakage to make land contamination, the Main Contractor was advised to remove it or placed it into drip tray. 	<ul style="list-style-type: none"> The new NRMM label has been post on generator. Oil drum has placed inside drip tray; deficiency has rectified.
23 Dec 2021	<ul style="list-style-type: none"> Air compressor without noise emission label was observed. The Main Contractor has been advised that noise emission label shall provide all air compressor as used within site area. 	<ul style="list-style-type: none"> During site inspection dated on 29th Dec 2021 to observe that all air compressor as used within site area has been post noise emission label
29 Dec 2021	<ul style="list-style-type: none"> All soil stockpiles if greater than 50m³, it shall cover with plastic sheets and maintenance to prevent fine particles soil emission Although dust general mitigation measures have been provided, however dust emission is observed during piling work underway. Enhancement dust mitigation measures e.g. piling work area increase watering frequencies or the mouth of piling borehole covering impervious sheets. General refuse observed on existing ground. Waste skip shall be to provide for storage. 	<p>To be report in next reporting month</p> <p>To be report in next reporting month</p> <p>To be report in next reporting month</p>

8. ENVIRONMENTAL COMPLAINT AND NON-COMPLIANCE

8.1 ENVIRONMENTAL COMPLAINT, SUMMONS AND PROSECUTION

8.1.1 For the Contract Works, no environmental complaint, summons and prosecution was received in the Reporting Period. The statistical summary table of environmental complaint is presented in *Tables 8-1-1, 8-1-2* and *8-1-3*.

Table 8-1-1 Statistical Summary of Environmental Complaints

Reporting Period	Environmental Complaint Statistics		
	Frequency	Cumulative	Complaint Nature
7 – 31 December 2021	0	0	NA

Table 8-1-2 Statistical Summary of Environmental Summons

Reporting Period	Environmental Summons Statistics		
	Frequency	Cumulative	Complaint Nature
7 – 31 December 2021	0	0	NA

Table 8-1-3 Statistical Summary of Environmental Prosecution

Reporting Period	Environmental Prosecution Statistics		
	Frequency	Cumulative	Complaint Nature
7 – 31 December 2021	0	0	NA

9. IMPLEMENTATION STATUS OF MITIGATION MEASURES

9.1 GENERAL REQUIREMENTS

9.1.1 The environmental mitigation measures that recommended in the Implementation Schedule for Environmental Mitigation Measures (ISEMM) in the approved Updated EM&A Manual covered the issues of dust, noise, water, ecological and waste and they are summarized presented in [Appendix J](#).

9.1.2 The Contract Works shall be implementing the required environmental mitigation measures according to the approved Updated EM&A Manual as subject to the site condition. Environmental mitigation measures generally implemented by the Main Contractor in this Reporting Month are summarized in [Table 9-1-1](#).

Table 9-1-1 Environmental Mitigation Measures

Issues	Environmental Mitigation Measures
Water Quality	<ul style="list-style-type: none"> Wastewater to be treated by filtration system such as sedimentation tank and storage on-site. After Wastewater Discharge Permit is obtained to carry out dispose.
Air Quality	<ul style="list-style-type: none"> Maintain damp / wet surface on access road Keep slow speed in the sites All vehicles must use wheel washing facility before off site Sprayed water during breaking or excavation works Soil stockpile greater than 50m³ has cover with plastic sheets
Noise	<ul style="list-style-type: none"> Restrain operation time of plants from 07:00 to 19:00 on any working day except for Public Holiday and Sunday. Keep good maintenance of plants Shut down the plants when not in used.
Waste and Chemical Management	<ul style="list-style-type: none"> Follow requirements and procedures of the “Trip-ticket System” The site was generally kept tidy and clean.

9.2 TENTATIVE CONSTRUCTION ACTIVITIES IN THE COMING MONTH

9.2.1 The construction works under the Contract Works in the coming month are listed below:

- Site formation works
- Piling Work

9.3 KEY ISSUES FOR THE COMING MONTH

9.3.1 Key issues to be considered in the coming month for the Contract Works include:

- Implementation of control measures for rainstorm;
- Regular clearance of stagnant water during wet season;
- Implementation of dust suppression measures at all times;
- Potential wastewater quality impact due to surface runoff;
- Potential fugitive dust quality impact due from the dry/loose/exposure soil surface/dusty material;
- Disposal of empty engine oil containers within site area;
- Ensure dust suppression measures are implemented properly;
- Sediment catch-pits and silt removal facilities should be regularly maintained;
- Management of chemical wastes;
- Follow-up of improvement on general waste management issues; and
- Implementation of construction noise preventative control measures

9.3.2 The Main contractor should pay special attention on noise and dust and water quality mitigation measures and fully implement according to the ISEMM of the approved Updated EM&A Manual.

10. CONCLUSIONS AND RECOMMENDATIONS

10.1 CONCLUSIONS

- 10.1.1 This is **1st** monthly EM&A report presenting the monitoring results and inspection findings for the Reporting Period from **7** to **31 December 2021**.
- 10.1.2 No noise complaint (which is an Action Level exceedance) was received and no construction noise measurement results that exceeded the Limit Level were recorded in the Reporting Period. No NOEs or the associated corrective actions were therefore issued.
- 10.1.3 No documented complaint, notification of summons or successful prosecution was received by either the RE or CEDD or the Main Contractor.
- 10.1.4 Weekly site inspection by the RE, ET and the Main Contractor had carried out on **9, 16, 23** and **29 December 2021**. The mitigation measures implemented was considered satisfactory. No non-compliance observed during the site inspection.
- 10.1.5 Since the Contract Works is a New Engineering Contract (NEC) under Works Bureau of Public Works Projects in Hong Kong, and the appointment of the qualified Ecologist is yet to be completed by the Main Contractor and the Resident Engineer to undertake the ecology of waterbirds monitoring. Therefore, no waterbirds survey was carried out in the Reporting Month under this Contract.
- 10.1.6 Although waterbirds survey was not carried out by this Contract in the Reporting Month, a waterbird survey with similar approach was conducted by nearby DSD Project Agreement No. SPW 12/2021 Shek Wu Hui Effluent Polishing Plant – Main Works under Further Environmental Permit No. FEP-02/474/2013. According to the waterbird survey result conducted by the abovementioned DSD Project, no significant decrease of waterbird was recorded and therefore it is concluded that no disturbance to waterbird was caused by this Contract in the Reporting Month.

10.2 RECOMMENDATIONS


- 10.2.1 During dry season and in consideration of construction site under the Contract Works is located adjacent to villages, the Main Contractor should fully implement air quality mitigation measures to reduce construction dust emission.
- 10.2.2 Construction noise would be a key environmental issue during construction work of the Contract Works. Noise mitigation measures such as using quiet plants should be implemented in accordance with the approved Updated EM&A Manual requirement.
- 10.2.3 In addition, all effluent discharge shall after be obtained the Discharge Permit and shall necessary to compliance with Technical Memorandum of Effluent Discharged into Drainage and Sewerage Systems, inland and Coastal Waters criteria or discharge permits stipulation.
- 10.2.4 Moreover, mosquito control should be implemented to prevent mosquito breeding on site; and daily cleaning and weekly tidiness shall properly perform and maintenance.

Appendix A

Location of Shek Wu Hui Water Reclamation Plant

NOTES:
COPYRIGHT RESERVED
 THIS PRINT MAY NOT BE COPIED, TRACED, OR EXHIBITED WITHOUT PERMISSION OF THE WATER AUTHORITY.

- ALL DIMENSIONS ARE IN MILLIMETRES UNLESS OTHERWISE SPECIFIED.
- THE BASE PLAN IS EXTRACTED FROM SURVEY SHEET NOS. 2-SE AND 3-SW.

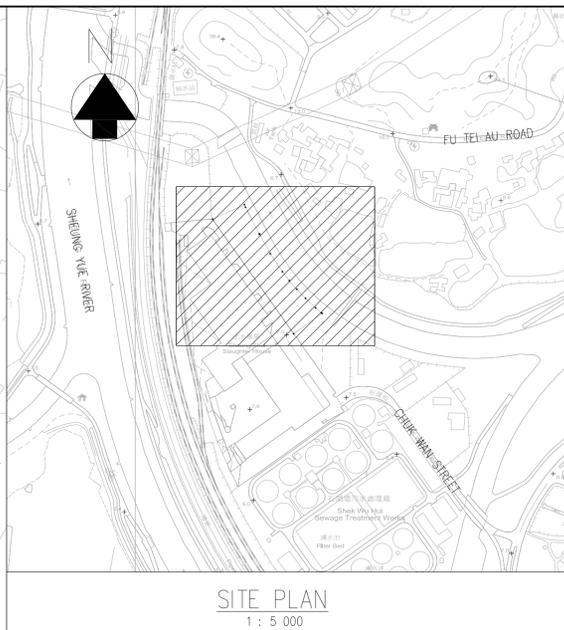

SETTING OUT INFORMATION

REFERENCE POINT	EASTING	NORTHING
A01	830108.97	841700.04
A02	830154.01	841720.67
A03	830155.48	841717.13
A04	830174.92	841679.59
A05	830175.60	841678.76
A06	830190.57	841651.38
A07	830207.66	841626.12
A08	830217.38	841613.54
A09	830227.94	841601.39
A10	830240.46	841588.45
A11	830254.44	841575.16
A12	830262.64	841568.06
A13	830263.90	841567.22
A14	830223.55	841538.61

Revision	Date	Description			Initial
		Designed	Checked	Drawn	
Initial		CWC	WH	SZ	GC
Date	02/21	02/21	02/21	02/21	02/21

Approved:


Contract No. 3/WSD/20

Contract Title
 RECLAIMED WATER SUPPLY TO SHEUNG SHUI AND FANLING

Drawing Title
**SWHWRP
 (PART 1 OF THE SITE) –
 SETTING OUT PLAN**

Drawing No. 401582/B&V/WRP/GN/201


Scale A1 1:400
 A3 1:800

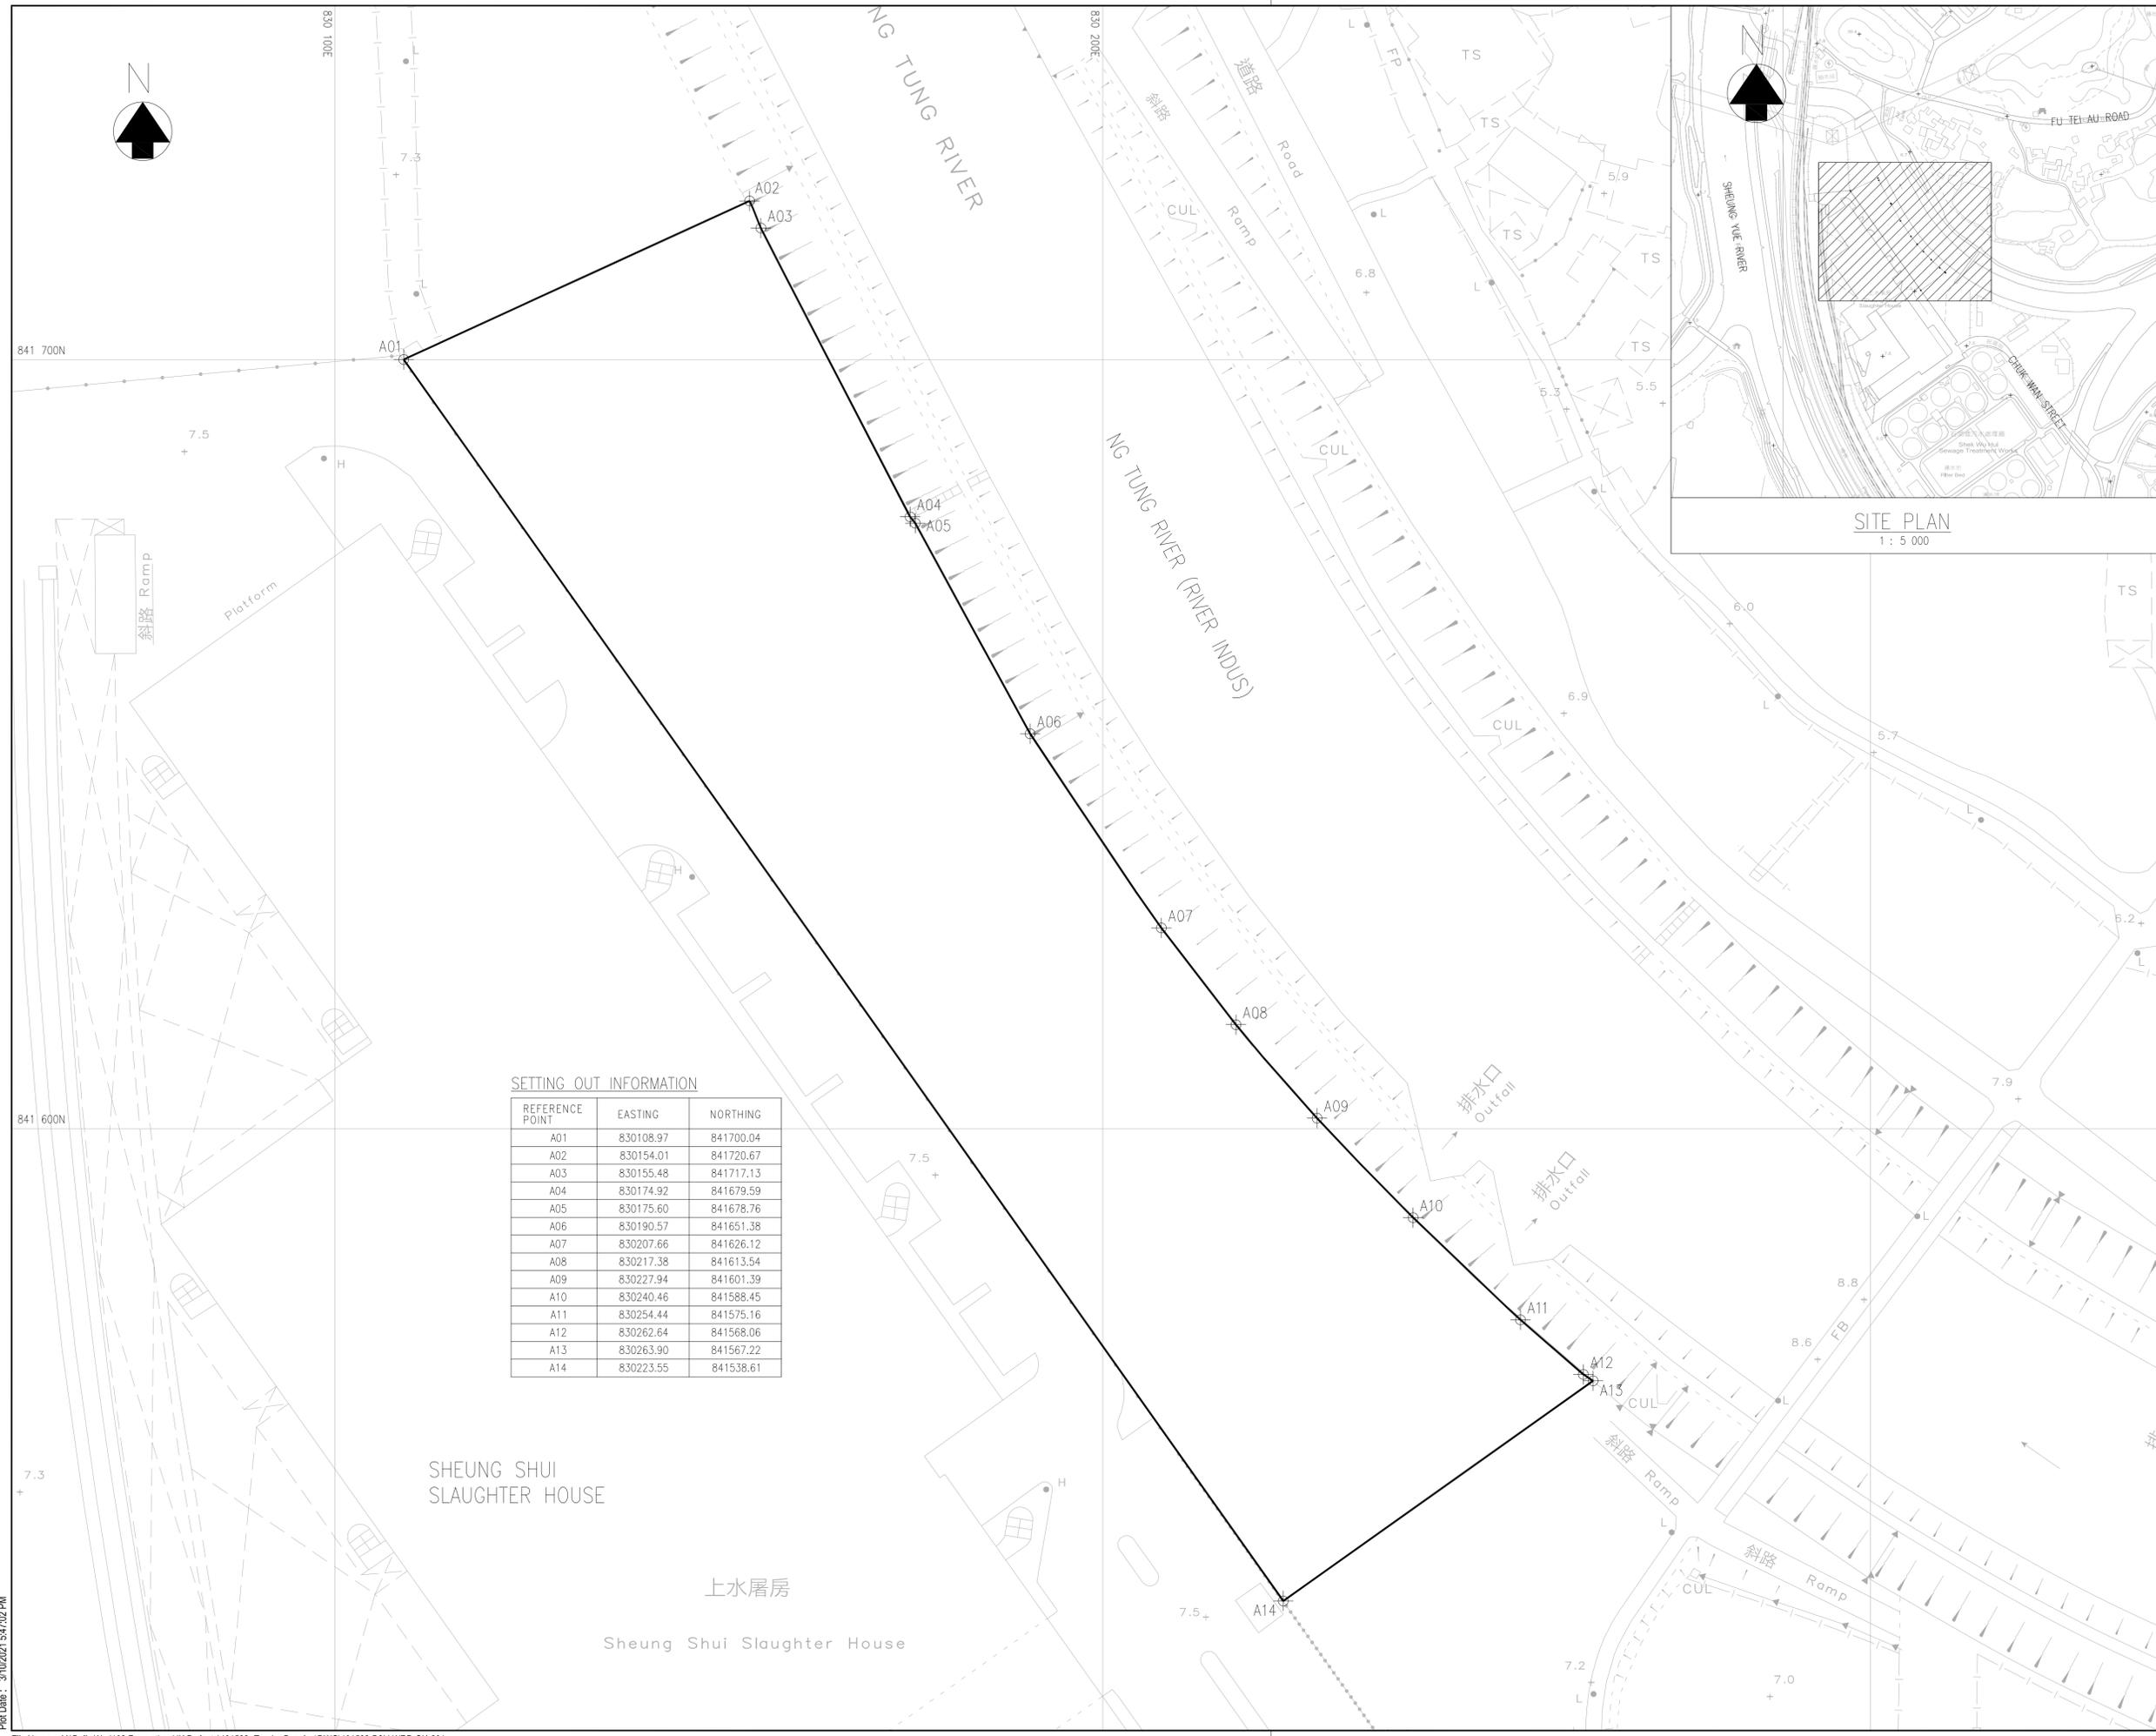

Appendix B

Project Organization

Project Organization Chart

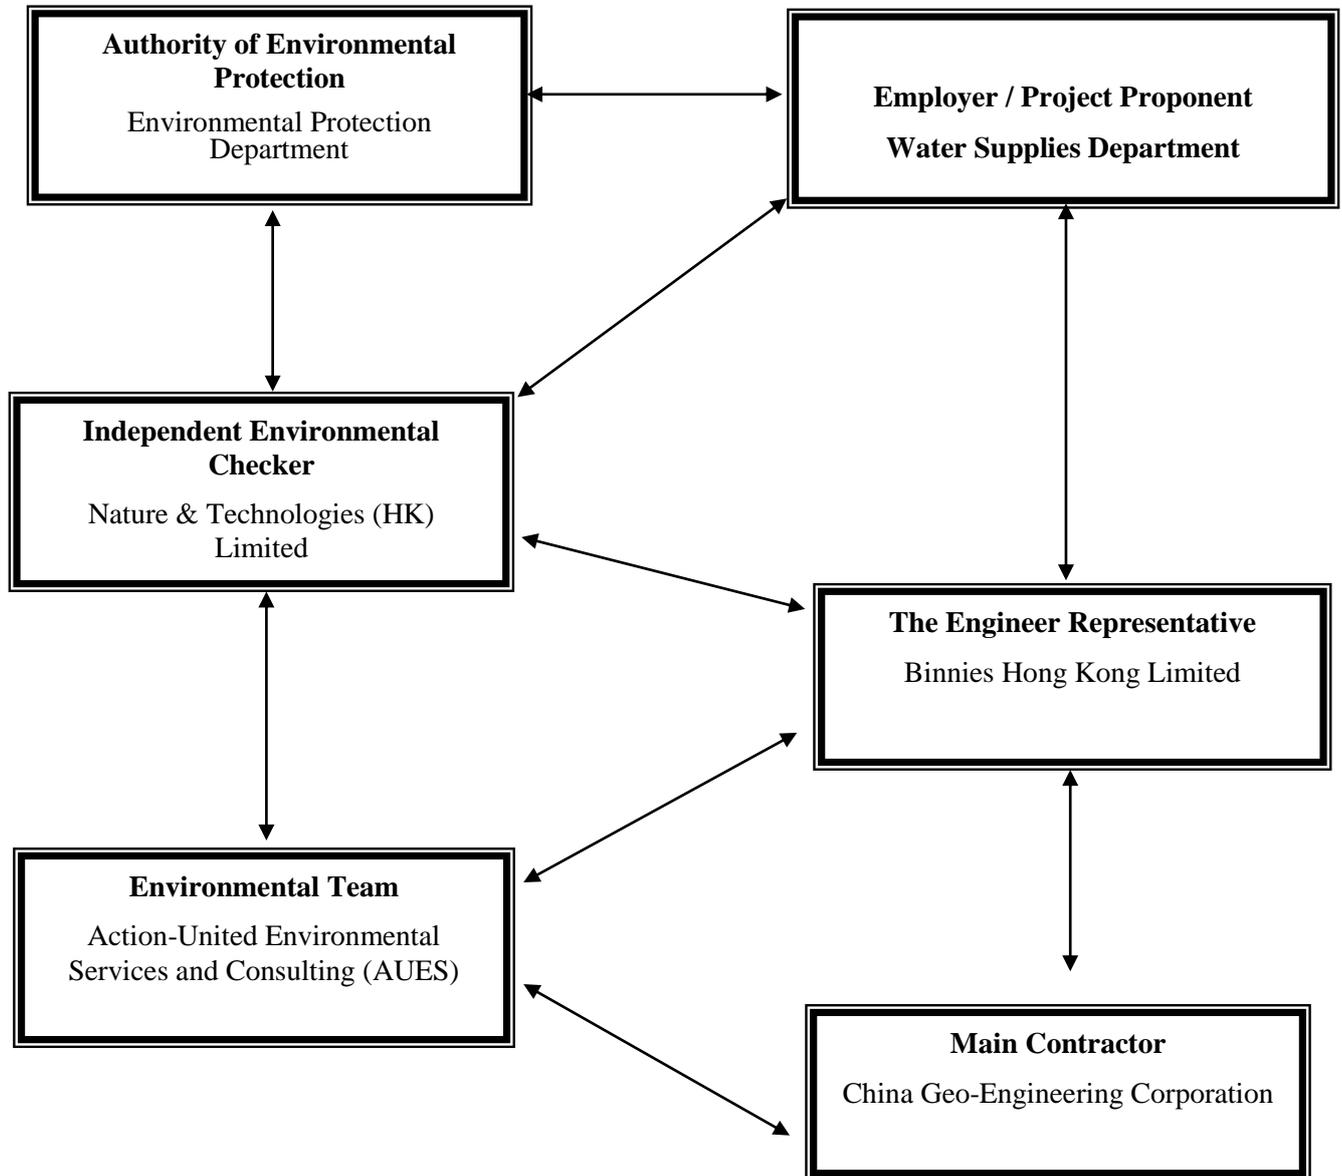

Contact Details of Key Personnel for the Project

Organization	Project Role	Name of Key Staff	Tel No.	Fax No.
WSD	Project Proponent	Tim Wong	2829 5638	2586 1696
Binnies	Resident Engineer	S.H. Chung	2608 7380	TBC
Binnies	Resident Engineer	Chester Chan,	2608 7380	TBC
N&T	Independent Environmental Checker	Vega Wong	2877 3122	2511 0922
CGC	Site Agent	Kelvin Tsoi	5211 3332	TBC
CGC	Environmental Officer	Luke Chung	6488 0975	TBC
AUES	Environmental Team Leader	T. W. Tam	2959 6059	2959 6079
AUES	Environmental Consultant	Nicola Hon	2959 6059	2959 6079
AUES	Environmental Consultant	Martin Li	2959 6059	2959 6079
AUES	Assistant Environmental Consultant	Fai So	2959 6059	2959 6079

Legend:

WSD (Employer) – Water Supplies Department

Binnies (Engineer Representative) – Binnies Hong Kong Limited

CGC (Main Contractor) – China Geo-Engineering Corporation

N&T (IEC) – Nature & Technologies (HK) Limited

AUES (ET) – Action-United Environmental Services and Consulting (AUES)

Appendix C

Master Construction Program

ID	Task Name	Duration	Start	Finish	TRA	Notes	2022			2023				2024				2025				2026			
							Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	
1	Contract Key Dates	1676 days	Jul 30 '21	Mar 1 '26																					
2	Contract Date	1 day	Jul 30 '21	Jul 30 '21																					
3	Starting Date	1 day	Jul 30 '21	Jul 30 '21																					
4	Contract Period	1675 days	Jul 31 '21	Mar 1 '26																					
5	Section 1 - Shek Wu Hui Water Reclamation Plant (SWHWRP)	791 days	Jul 31 '21	Sep 29 '23																					
6	Section 2 - Landscaping works of SWHWRP	791 days	Jul 31 '21	Sep 29 '23																					
7	Section 3 - Modification of Table Hill Reclaimed Water Service Reservoir	791 days	Jul 31 '21	Sep 29 '23																					
8	Section 4 - Mainlaying works in part 3 of the Site	791 days	Jul 31 '21	Sep 29 '23																					
9	Section 5 - Mainlaying works in part 4 of the Site	1095 days	Jul 31 '21	Jul 29 '24																					
10	Section 6 - Mainlaying works in part 5 of the Site	1279 days	Jul 31 '21	Jan 29 '25																					
11	Section 7 - Mainlaying works in part 6 of the Site	1522 days	Jul 31 '21	Sep 29 '25																					
12	Section 8 - Mainlaying works in part 7 of the Site & remaining WM works	1675 days	Jul 31 '21	Mar 1 '26																					
13	Section 9 - Conversion works of reclaimed water	1675 days	Jul 31 '21	Mar 1 '26																					
14	Contract Completion date	0 days	Mar 1 '26	Mar 1 '26																					
15																									
16	Preliminary & General	1062 days	Jul 30 '21	Jun 25 '24																					
17	Submission of Draft Safety Plan	14 days	Jul 30 '21	Aug 12 '21																					
18	Submission of Draft Environmental Management Plan	14 days	Jul 30 '21	Aug 12 '21																					
19	Submission of Sub-contractor Management Plan	14 days	Jul 30 '21	Aug 12 '21																					
20	Notification & request for UU record from utility undertakers	14 days	Jul 30 '21	Aug 12 '21																					
21	Submission and acceptance of selection procedure for supplier	29 days	Aug 3 '21	Aug 31 '21																					
22	Submission and acceptance of selection procedure for subcontractor	35 days	Aug 3 '21	Sep 6 '21																					
23	Agreement on preliminary office layout	35 days	Aug 12 '21	Sep 15 '21																					
24	Provision of Project Manager's Accommodation	152 days	Sep 10 '21	Feb 8 '22																					
25	Submission and acceptance of subletting package	14 days	Sep 10 '21	Sep 23 '21																					
26	Selection of Subcontractor	18 days	Sep 24 '21	Oct 11 '21																					
27	Erection of Project Manager's Accommodation	120 days	Oct 12 '21	Feb 8 '22																					
28	Selection of Traffic Consultant	1027 days	Sep 3 '21	Jun 25 '24																					
29	Submission and acceptance of subletting package	14 days	Sep 3 '21	Sep 16 '21																					
30	Selection of traffic consultant	13 days	Sep 17 '21	Sep 29 '21																					
31	XP application for different Sections	1000 days	Sep 30 '21	Jun 25 '24																					
32	TTA application for different Sections	1000 days	Sep 30 '21	Jun 25 '24																					
33	Selection of Concrete Supplier	29 days	Sep 6 '21	Oct 4 '21																					
34	Submission and acceptance of subletting package	9 days	Sep 6 '21	Sep 14 '21																					
35	Selection of concrete supplier	20 days	Sep 15 '21	Oct 4 '21																					
36	Selection of Subcontractor for Excavation and ELS Works at SWHWRP	42 days	Oct 7 '21	Nov 17 '21																					
37	Submission and acceptance of subletting package	21 days	Oct 7 '21	Oct 27 '21																					
38	Selection of subcontractor	21 days	Oct 28 '21	Nov 17 '21																					
39	Selection of Subcontractor for Structural Works	39 days	Dec 1 '21	Jan 8 '22																					
40	Submission and acceptance of subletting package	21 days	Dec 1 '21	Dec 21 '21																					
41	Selection of subcontractor	18 days	Dec 22 '21	Jan 8 '22																					
42	Selection of Subcontractor for Mainlaying Works	35 days	Dec 1 '21	Jan 4 '22																					
43	Submission and acceptance of subletting package - open trench	21 days	Dec 1 '21	Dec 21 '21																					
44	Selection of subcontractor - open trench	14 days	Dec 22 '21	Jan 4 '22																					
45	Submission and acceptance of subletting package - trenchless	21 days	Dec 1 '21	Dec 21 '21																					
46	Selection of subcontractor - trenchless	14 days	Dec 22 '21	Jan 4 '22																					
47																									
48	Section 1 & 2 - Construction of SWHWRP and Landscaping Works	764 days	Aug 27 '21	Sep 29 '23																					

Project: 3WSD20 Programme
Date: Nov 29 '21

Task		Inactive Task		Manual Summary Rollup		External Milestone		Manual Progress	
Split		Inactive Milestone		Manual Summary		Deadline			
Milestone		Inactive Summary		Start-only		Critical			
Summary		Manual Task		Finish-only		Critical Split			
Project Summary		Duration-only		External Tasks		Progress			


ID	Task Name	Duration	Start	Finish	TRA	Notes	2022			2023			2024			2025			2026				
							Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2
97	Construction of Beams and Slabs at +9.1mPD	30 days	Mar 4 '23	Apr 2 '23																			
98	Construction of Beams and Slabs at +15.2mPD	60 days	Apr 3 '23	Jun 1 '23																			
99	Construction of Parapet Walls (+15.2mPD to +16.6mPD)	21 days	Jun 2 '23	Jun 22 '23																			
100	Construction of Staircase ST3 (+13.5mPD to +15.45mPD)	21 days	Jun 2 '23	Jun 22 '23																			
101	Construction of RC structure of HCF	367 days	Jun 20 '22	Jun 21 '23																			
102	Construction of Superstructure (above ground) - Grid Line 1-3	113 days	Jun 20 '22	Oct 10 '22																			
103	Construction of Columns (+5.55mPD to +13.00mPD)	14 days	Jun 20 '22	Jul 3 '22																			
104	Construction of Wall W8 (+5.8mPD to +10.4mPD)	14 days	Jul 4 '22	Jul 17 '22																			
105	Construction of Bearing walls and Slabs (+5.55mPD to +7.1mPD)	14 days	Jul 18 '22	Jul 31 '22																			
106	Construction of Columns (+10.4mPD to +13.00mPD)	7 days	Aug 1 '22	Aug 7 '22																			
107	Construction of Beams and Slabs at +13.00mPD	50 days	Aug 8 '22	Sep 26 '22																			
108	Construction of Parapet Walls (+13.00mPD to +15.1mPD)	14 days	Sep 27 '22	Oct 10 '22																			
109	Construction of Superstructure (above ground) - Grid Line 3-7	254 days	Oct 11 '22	Jun 21 '23																			
110	Construction of Columns (+4.55mPD to +10.8mPD)	7 days	Oct 11 '22	Oct 17 '22																			
111	Construction of Walls W1, W7, W19, W20, W29	21 days	Oct 18 '22	Nov 7 '22																			
112	Construction of Walls W9, W13, W14, W37, W38	10 days	Nov 8 '22	Nov 17 '22																			
113	Construction of Walls W2 to W6	28 days	Nov 18 '22	Dec 15 '22																			
114	Construction of Walls W10, W11, W15, W16, W12, W35, W36	10 days	Dec 16 '22	Dec 25 '22																			
115	Construction of Beams and Slabs at +10.4mPD and +10.8mPD	150 days	Dec 26 '22	May 24 '23																			
116	Construction of Parapet Walls (+10.4mPD/+10.8mPD to +12.5mPD)	14 days	May 25 '23	Jun 7 '23																			
117	Construction of Staircase ST01 (+7.1mPD to +11.35mPD)	28 days	May 25 '23	Jun 21 '23																			
118	Construction of Staircase ST01 (+10.4mPD to +13.95mPD)	14 days	May 25 '23	Jun 7 '23																			
119	Installation of architectural works	120 days	Jun 2 '23	Sep 29 '23																			
120	Construction of roadworks (drainage, irrigation system, cable ducting, etc)	60 days	May 3 '23	Jul 1 '23																			
121	Construction of EVA (road pavement, fence wall, etc)	60 days	Jul 2 '23	Aug 30 '23																			
122	Landscape works	120 days	Jun 2 '23	Sep 29 '23																			
123	E&M Works of SWHWRP	712 days	Oct 18 '21	Sep 29 '23																			
124	Design and Submission Stage	140 days	Oct 18 '21	Mar 6 '22																			
125	Submission and acceptance of Surge Analysis Report	22 days	Oct 18 '21	Nov 8 '21																			
126	Submission and acceptance of Reclaimed Water Main Pumps	59 days	Oct 25 '21	Dec 22 '21																			
127	Submission and acceptance of Surge Vessels and Air Compressors	59 days	Oct 25 '21	Dec 22 '21																			
128	Submission and acceptance of Penstock & Stoplog	25 days	Oct 25 '21	Nov 18 '21																			
129	Submission and acceptance of Chemical Dosing System & Static In-line Mixer	42 days	Nov 9 '21	Dec 20 '21																			
130	Submission and acceptance of Air Blower and Air Diffuser	30 days	Oct 25 '21	Nov 23 '21																			
131	Submission and acceptance of Lifting Appliances	65 days	Oct 29 '21	Jan 1 '22																			
132	Submission and acceptance of Minor Mechanical Equipment	63 days	Oct 29 '21	Dec 30 '21																			
133	Submission and acceptance of LV switchboard	60 days	Oct 25 '21	Dec 23 '21																			
134	Submission and acceptance of DCS	81 days	Oct 25 '21	Jan 13 '22																			
135	Submission and acceptance of Instrumentation & Water Monitoring Equipment	42 days	Oct 29 '21	Dec 9 '21																			
136	Submission and acceptance of Misc. Electrical Items	72 days	Nov 13 '21	Jan 23 '22																			
137	Submission and acceptance of Fire Services Equipment	126 days	Nov 1 '21	Mar 6 '22																			
138	Submission and acceptance of MVAC Equipment	87 days	Nov 1 '21	Jan 26 '22																			
139	Submission and acceptance of Plumbing & Drainage Equipment	87 days	Nov 1 '21	Jan 26 '22																			
140	Submission and acceptance of General Arrangement Drawing	101 days	Oct 29 '21	Feb 6 '22																			
141	Submission and acceptance of Civil Requirement Drawing	56 days	Nov 27 '21	Jan 21 '22																			
142	Procurement and Delivery of Equipment	345 days	Nov 19 '21	Oct 29 '22																			
143	Reclaimed Water Main Pumps (6 nos.)	330 days	Nov 25 '21	Oct 20 '22																			
144	Surge Vessels and Air Compressors	270 days	Dec 23 '21	Sep 18 '22																			

Project: 3WSD20 Programme
Date: Nov 29 '21

Task		Inactive Task		Manual Summary Rollup		External Milestone		Manual Progress	
Split		Inactive Milestone		Manual Summary		Deadline			
Milestone		Inactive Summary		Start-only		Critical			
Summary		Manual Task		Finish-only		Critical Split			
Project Summary		Duration-only		External Tasks		Progress			

Appendix D

Location of Designated Noise Monitoring Station CP-KTN-NMS5

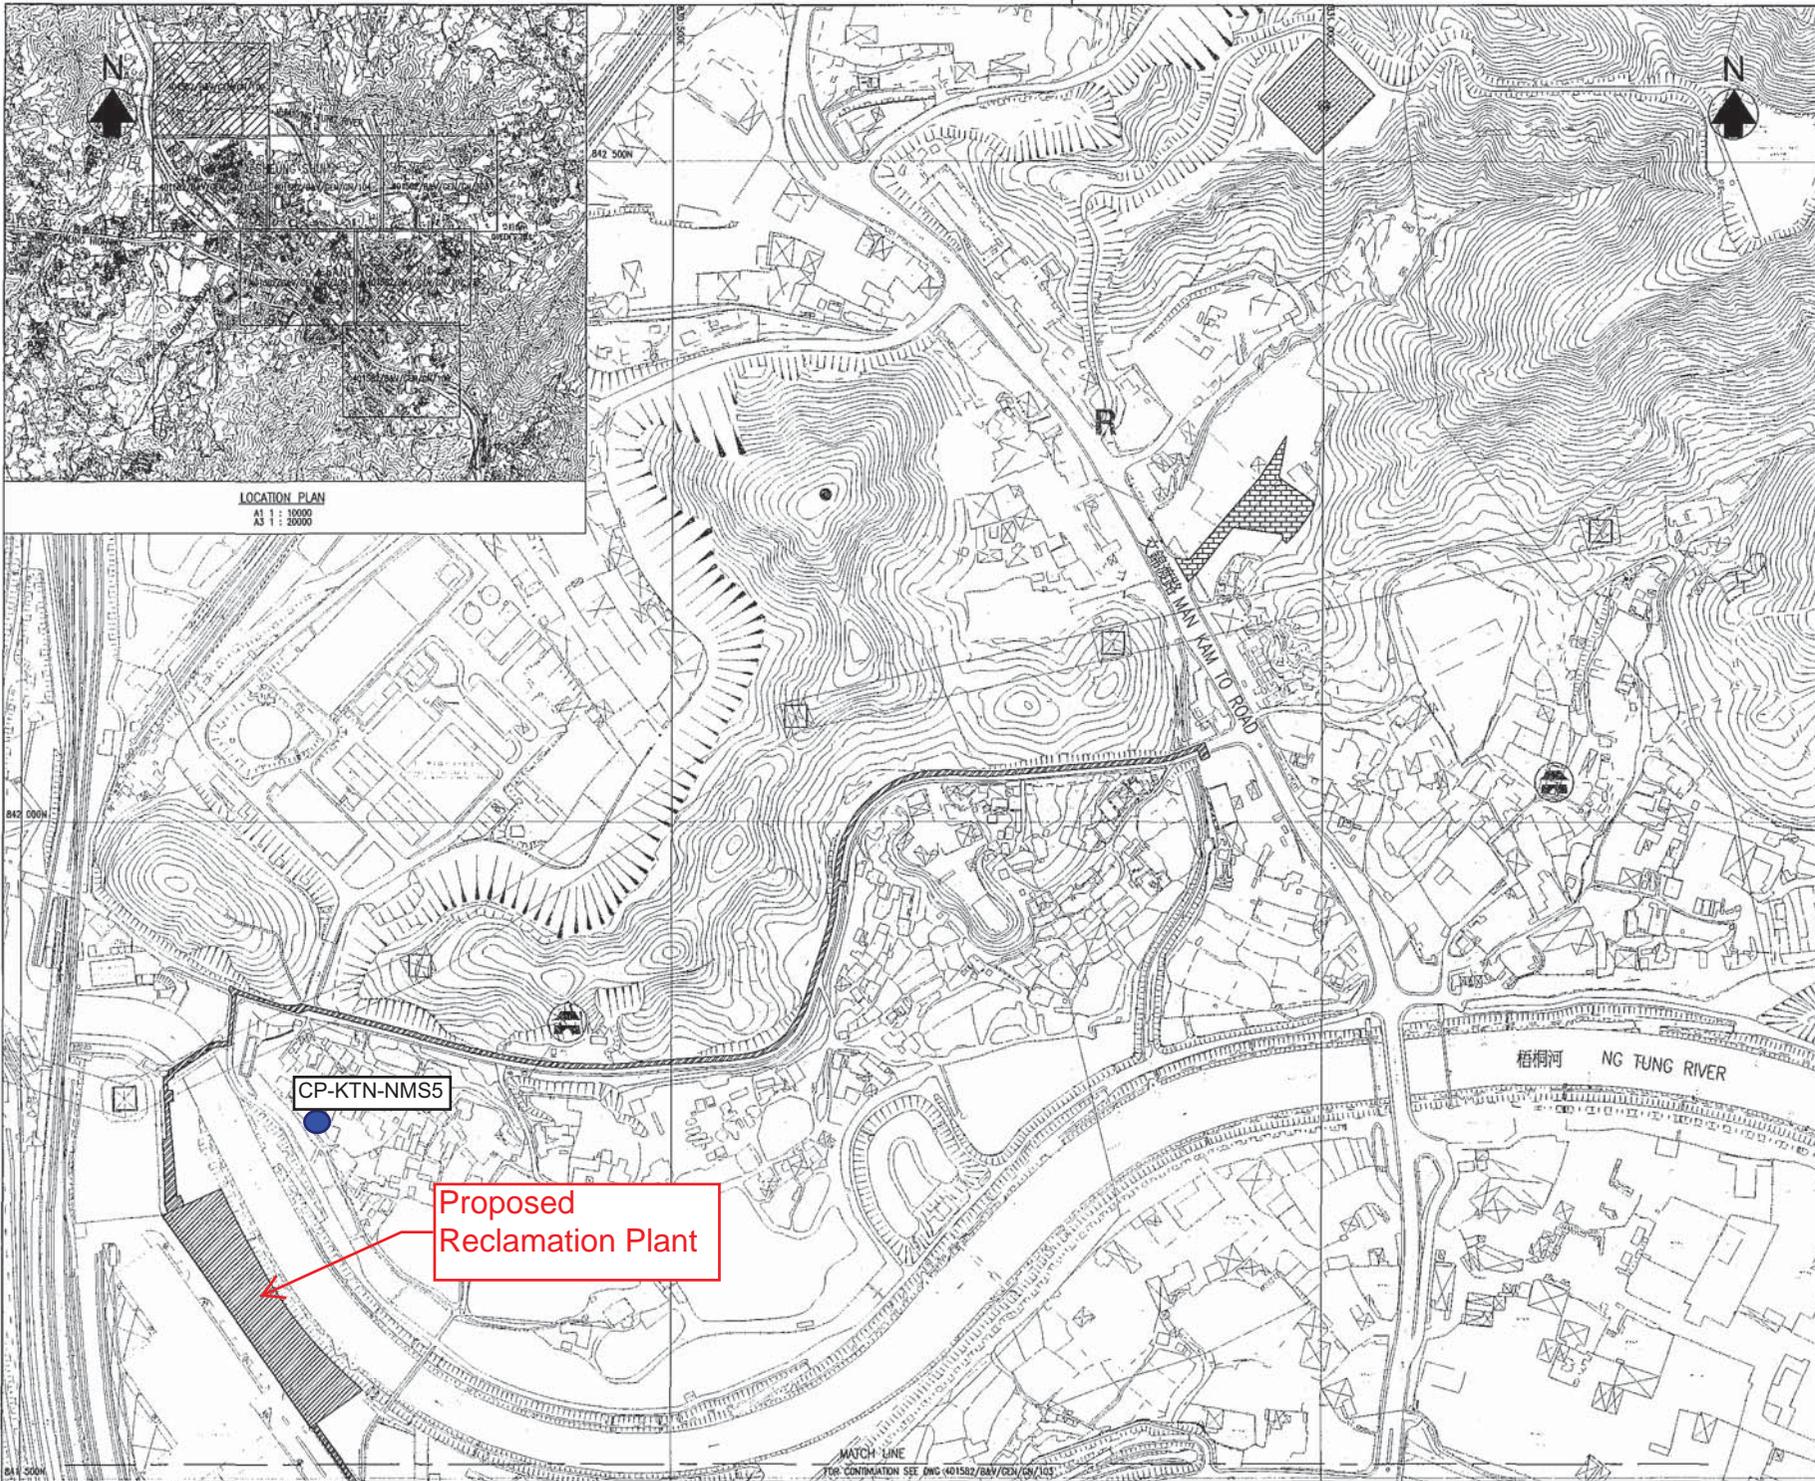

NOTES:

1. ALL LEVELS ARE IN REFERENCE TO METRES ABOVE THE HONG KONG PRINCIPAL DATUM (mPD) UNLESS OTHERWISE STATED.
2. FOR GENERAL NOTES, REFER TO 401582/BAW/GEN/GN/001
3. ALL DIMENSIONS ARE IN MILLIMETRES UNLESS OTHERWISE SPECIFIED.

COPYRIGHT RESERVED

THIS PRINT MAY NOT BE COPIED, TRACED, OR EXHIBITED WITHOUT PERMISSION OF THE WATER AUTHORITY.

1. THE BASE PLAN IS EXTRACTED FROM SURVEY SHEET NOS. 2-NE, 2-SE, 3AW AND 3-SW.

LEGEND:

- PART 1 OF THE SITE
- PART 2 OF THE SITE
- PART 3 OF THE SITE
- PART 4 OF THE SITE
- PART 5 OF THE SITE
- PART 6 OF THE SITE
- PART 7 OF THE SITE
- PART W1 OF THE SITE

Station	Date		Erection		W/E	
	Request	Checked	Drawn	Checked		
W101	CWC	WH	SZ	CC		
Date	02/21	02/21	02/21	02/21		

Approved:

Contract No. 3/WSD/20

Contract Title
RECLAIMED WATER SUPPLY TO SHEUNG SHUI AND FANLING

Drawing Title

Noise Monitoring Station

Appendix E

Valid Calibration Certificates of Monitoring Equipment



輝創工程有限公司

Sun Creation Engineering Limited
Calibration & Testing Laboratory

Certificate of Calibration 校正證書

Certificate No. : C210389
證書編號

ITEM TESTED / 送檢項目 (Job No. / 序引編號 : IC21-0122) Date of Receipt / 收件日期 : 19 January 2021

Description / 儀器名稱 : Sound Level Meter (EQ018)
Manufacturer / 製造商 : Rion
Model No. / 型號 : NL-52
Serial No. / 編號 : 00809405
Supplied By / 委託者 : Action-United Environmental Services and Consulting
Unit A, 20/F., Gold King Industrial Building,
35-41 Tai Lin Pai Road, Kwai Chung, N.T.

TEST CONDITIONS / 測試條件

Temperature / 溫度 : $(23 \pm 2)^{\circ}\text{C}$ Relative Humidity / 相對濕度 : $(50 \pm 25)\%$
Line Voltage / 電壓 : ---

TEST SPECIFICATIONS / 測試規範

Calibration check

DATE OF TEST / 測試日期 : 20 January 2021


TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.
The results do not exceed manufacturer's specification.
The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via :

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- The Bruel & Kjaer Calibration Laboratory, Denmark
- Agilent Technologies / Keysight Technologies
- Fluke Everett Service Center, USA

Tested By : 
測試 : K P Cheuk
Assistant Engineer

Certified By : 
核證 : K C Lee
Engineer

Date of Issue : 20 January 2021
簽發日期

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory

c/o 4/F, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

輝創工程有限公司 - 校正及檢測實驗室

c/o 香港新界屯門興安里一號四樓

Tel/電話: (852) 2927 2606 Fax/傳真: (852) 2744 8986

E-mail/電郵: callab@suncreation.com

Website/網址: www.suncreation.com

Certificate of Calibration

校正證書

Certificate No. : C210389
證書編號

1. The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours, and switched on to warm up for over 10 minutes before the commencement of the test.
2. Self-calibration was performed before the test.
3. The results presented are the mean of 3 measurements at each calibration point.
4. Test equipment :

<u>Equipment ID</u>	<u>Description</u>	<u>Certificate No.</u>
CL280	40 MHz Arbitrary Waveform Generator	C210084
CL281	Multifunction Acoustic Calibrator	CDK1806821

5. Test procedure : MA101N.

6. Results :

- 6.1 Sound Pressure Level

- 6.1.1 Reference Sound Pressure Level

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)		
30 - 130	L _A	A	Fast	94.00	1	94.1	± 1.1

- 6.1.2 Linearity

UUT Setting				Applied Value		UUT Reading (dB)
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	
30 - 130	L _A	A	Fast	94.00	1	94.1 (Ref.)
				104.00		104.1
				114.00		114.1

IEC 61672 Class 1 Spec. : ± 0.6 dB per 10 dB step and ± 1.1 dB for overall different.

- 6.2 Time Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)		
30 - 130	L _A	A	Fast	94.00	1	94.1	Ref.
			Slow			94.1	± 0.3

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。

Certificate of Calibration

校正證書

Certificate No. : C210389
證書編號

6.3 Frequency Weighting

6.3.1 A-Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq.		
30 - 130	L _A	A	Fast	94.00	63 Hz	67.8	-26.2 ± 1.5
					125 Hz	77.9	-16.1 ± 1.5
					250 Hz	85.4	-8.6 ± 1.4
					500 Hz	90.9	-3.2 ± 1.4
					1 kHz	94.1	Ref.
					2 kHz	95.3	+1.2 ± 1.6
					4 kHz	95.1	+1.0 ± 1.6
					8 kHz	93.1	-1.1 (+2.1 ; -3.1)
					12.5 kHz	89.7	-4.3 (+3.0 ; -6.0)

6.3.2 C-Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq.		
30 - 130	L _C	C	Fast	94.00	63 Hz	93.3	-0.8 ± 1.5
					125 Hz	93.9	-0.2 ± 1.5
					250 Hz	94.1	0.0 ± 1.4
					500 Hz	94.1	0.0 ± 1.4
					1 kHz	94.1	Ref.
					2 kHz	93.9	-0.2 ± 1.6
					4 kHz	93.3	-0.8 ± 1.6
					8 kHz	91.2	-3.0 (+2.1 ; -3.1)
					12.5 kHz	87.7	-6.2 (+3.0 ; -6.0)

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。



Certificate of Calibration

校正證書

Certificate No. : C210389
證書編號

Remarks : - UUT Microphone Model No. : UC-59 & S/N : 16463

- Mfr's Spec. : IEC 61672 Class 1

- Uncertainties of Applied Value :

94 dB	: 63 Hz - 125 Hz	: ± 0.35 dB
	250 Hz - 500 Hz	: ± 0.30 dB
	1 kHz	: ± 0.20 dB
	2 kHz - 4 kHz	: ± 0.35 dB
	8 kHz	: ± 0.45 dB
	12.5 kHz	: ± 0.70 dB
104 dB	: 1 kHz	: ± 0.10 dB (Ref. 94 dB)
114 dB	: 1 kHz	: ± 0.10 dB (Ref. 94 dB)

- The uncertainties are for a confidence probability of not less than 95 %.

Note :

Only the original copy or the laboratory's certified true copy is valid.

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory

c/o 4/F, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

輝創工程有限公司 - 校正及檢測實驗室

c/o 香港新界屯門興安里一號四樓

Tel/電話: (852) 2927 2606 Fax/傳真: (852) 2744 8986

E-mail/電郵: callab@suncreation.com

Website/網址: www.suncreation.com



Certificate of Calibration 校正證書

Certificate No. : C214361
證書編號

ITEM TESTED / 送檢項目 (Job No. / 序引編號 : IC21-1345)

Date of Receipt / 收件日期 : 8 July 2021

Description / 儀器名稱 : Sound Calibrator (EQ082)
Manufacturer / 製造商 : Brüel & Kjær
Model No. / 型號 : 4231
Serial No. / 編號 : 2713428
Supplied By / 委託者 : Action-United Environmental Services and Consulting
Unit A, 20/F., Gold King Industrial Building,
35-41 Tai Lin Pai Road, Kwai Chung, N.T.

TEST CONDITIONS / 測試條件

Temperature / 溫度 : (23 ± 2)°C
Line Voltage / 電壓 : ---
Relative Humidity / 相對濕度 : (50 ± 25)%

TEST SPECIFICATIONS / 測試規範

Calibration check

DATE OF TEST / 測試日期 : 24 July 2021

TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.
The results do not exceed manufacturer's specification.
The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via :

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Agilent Technologies / Keysight Technologies
- Fluke Everett Service Center, USA

Tested By : 
測試 : _____
K P Cheuk
Project Engineer

Certified By : 
核證 : _____
K C Lee
Engineer

Date of Issue : 26 July 2021
簽發日期

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.
本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Certificate of Calibration

校正證書

Certificate No. : C214361
證書編號

- The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours before the commencement of the test.
- The results presented are the mean of 3 measurements at each calibration point.
- Test equipment :

<u>Equipment ID</u>	<u>Description</u>	<u>Certificate No.</u>
CL130	Universal Counter	C213954
CL281	Multifunction Acoustic Calibrator	AV210017
TST150A	Measuring Amplifier	C201309

- Test procedure : MA100N.

- Results :

5.1 Sound Level Accuracy

UUT Nominal Value	Measured Value (dB)	Mfr's Spec. (dB)	Uncertainty of Measured Value (dB)
94 dB, 1 kHz	94.0	± 0.2	± 0.2
114 dB, 1 kHz	114.1		

5.2 Frequency Accuracy

UUT Nominal Value (kHz)	Measured Value (kHz)	Mfr's Spec.	Uncertainty of Measured Value (Hz)
1	1.000 0	1 kHz ± 0.1 %	± 0.1

Remark : The uncertainties are for a confidence probability of not less than 95 %.

Note :

Only the original copy or the laboratory's certified true copy is valid.

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

Appendix F

Monitoring Schedule of the Reporting Month and Coming Month

The Reporting Monitoring Schedule (December 2021)

Date		Noise Monitoring (Leq30min)	Ecology Monitoring (Water Bird)*
Wed	1-Dec-21		
Thu	2-Dec-21		
Fri	3-Dec-21		
Sat	4-Dec-21		
Sun	5-Dec-21		
Mon	6-Dec-21		
Tue	7-Dec-21	<i>The Project commencement Date</i>	
Wed	8-Dec-21		
Thu	9-Dec-21		
Fri	10-Dec-21	✓	
Sat	11-Dec-21		
Sun	12-Dec-21		
Mon	13-Dec-21		
Tue	14-Dec-21		
Wed	15-Dec-21	✓	
Thu	16-Dec-21		
Fri	17-Dec-21		
Sat	18-Dec-21		
Sun	19-Dec-21		
Mon	20-Dec-21		
Tue	21-Dec-21		
Wed	22-Dec-21	✓	
Thu	23-Dec-21		
Fri	24-Dec-21		
Sat	25-Dec-21		
Sun	26-Dec-21		
Mon	27-Dec-21		
Tue	28-Dec-21		
Wed	29-Dec-21	✓	
Thu	30-Dec-21		
Fri	31-Dec-21		

Remark:

(*) Ecology monitoring still yet commenced

✓	Monitoring Day
	Sunday or Public Holiday

The Coming Month Monitoring Schedule (January 2022)

Date		Noise Monitoring (Leq30min)	Ecology Monitoring (Water Bird) ^{Note}
Sat	1-Jan-22		
Sun	2-Jan-22		
Mon	3-Jan-22		
Tue	4-Jan-22		✓
Wed	5-Jan-22		
Thu	6-Jan-22		
Fri	7-Jan-22	✓	
Sat	8-Jan-22		
Sun	9-Jan-22		
Mon	10-Jan-22		
Tue	11-Jan-22		✓
Wed	12-Jan-22		
Thu	13-Jan-22	✓	
Fri	14-Jan-22		
Sat	15-Jan-22		
Sun	16-Jan-22		
Mon	17-Jan-22		
Tue	18-Jan-22		
Wed	19-Jan-22	✓	
Thu	20-Jan-22		
Fri	21-Jan-22		✓
Sat	22-Jan-22		
Sun	23-Jan-22		
Mon	24-Jan-22		
Tue	25-Jan-22	✓	
Wed	26-Jan-22		
Thu	27-Jan-22		
Fri	28-Jan-22		✓
Sat	29-Jan-22		
Sun	30-Jan-22		
Mon	31-Jan-22		

Note:

Ecology monitoring dates are tentative and are subject to change

✓	Monitoring Day
	Sunday or Public Holiday


Appendix G

Database of Monitoring Result

Daytime Noise Measurement Results (dB) at CP-KTN-NMS5																					
Date	Start Time	1st Leq (5min)			2nd Leq (5min)			3rd Leq (5min)			4th Leq (5min)			5th Leq (5min)			6th Leq (5min)			Leq30min, dB(A)	Corrected Leq30min dB(A)
		Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)		
10-Dec-21	09:10	62.3	65.8	56.3	56.2	57.7	54.3	56.9	58.2	55.0	68.8	73.9	57.2	61.8	64.9	56.7	62.4	65.8	56.4	63.5	66.5
15-Dec-21	09:18	53.5	54.5	52.2	55.2	56.5	52.7	53.7	55.2	51.9	52.8	53.7	51.8	56.2	57.6	53.4	55.8	57.7	53.2	54.7	57.7
22-Dec-21	10:33	56.5	58.8	53.9	55.9	58.1	53.3	56.7	55.6	52.5	56.4	59.0	52.3	56.4	58.9	53.0	55.8	57.0	52.4	56.3	59.3
29-Dec-21	10:06	55.1	57.7	51.4	52.7	53.8	51.0	54.0	56.3	51.1	52.7	54.3	50.5	52.8	54.6	50.5	52.9	55.4	50.1	53.5	56.5

Appendix H

Graphical Plots for Monitoring Result

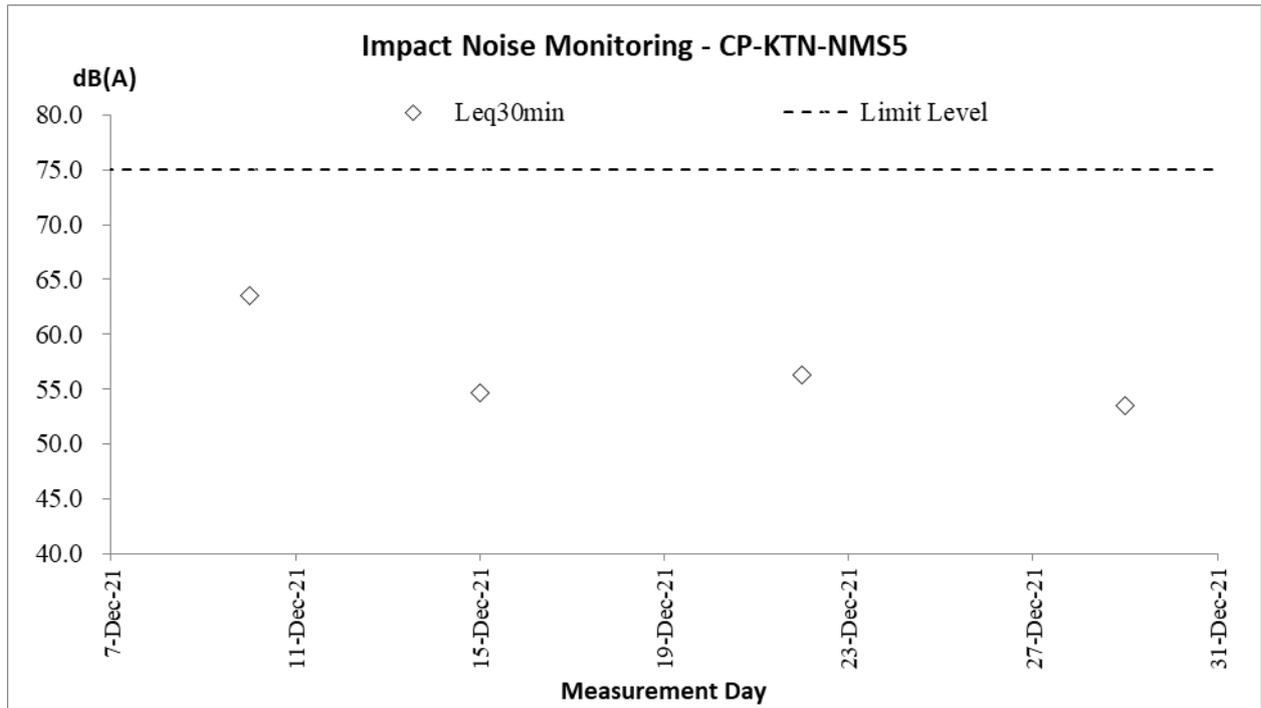

Appendix I

Monthly Summary Waste Flow Table

China Geo-Engineering Corporation

Contract No. : 3/WSD/20

Contact Name: Reclaimed Water Supply to Sheung Shui and Fanling

Monthly Summary Waste Flow Table for 2021 (year)

Month	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantities of C&D Wastes Generated Monthly				
	Total Quantity Generated	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard packaging	Plastics (see Note 3)	Chemical Waste	Others, e.g. general refuse
	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000 kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000m ³)
Jan											
Feb											
Mar											
Apr											
May											
June											
Sub-total											
July											
Aug	0	0	0	0	0	0	0	0	0	0	0
Sept	0	0	0	0	0	0	0	0	0	0	0
Oct	0	0	0	0	0	0	0	0	0	0	0
Nov	0	0	0	0	0	0	0	0	0	0	0
Dec	0.244	0	0	0	0.244	0	0	0	0	0	0
Total	0.244	0	0	0	0.244	0	0	0	0	0	0

Appendix J

Implementation Schedule for Environmental Mitigation Measures (ISEMM)

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the Measures?	Location of the measures	When to implement the Measures?	What requirements or standards for the measures to achieve?
Common Mitigation Measures (Applicable to ALL Project Components, including DPs and Non-DPs)							
Construction Dust Impact							
S3.8	D1	Mitigation measures in form of regular watering under a good site practice should be adopted. Watering once per hour on exposed worksites and haul road is proposed to achieve dust removal efficiency of 92.1%. While the above watering frequencies are to be followed, the extent of watering may vary depending on actual site conditions but should be sufficient to maintain an equivalent intensity of no less than 1.7 L/m ² to achieve the respective dust removal efficiencies.	Minimize dust impact at the nearby sensitive receivers	Contractor	All construction sites	Construction phase	APCO To control the dust impact to meet HKAQO and TM-EIAO
S3.8	D2	The Contractor shall follow the procedures and requirements given in the Air Pollution Control (Construction Dust) Regulation.	Minimize dust impact at the nearby sensitive receivers	Contractor	All construction sites	Construction phase	APCO To control the dust impact to meet HKAQO and TM-EIAO
S3.8	D3	Following dust suppression measures should also be incorporated by the Contractor to control the dust nuisance throughout the construction phase: <ul style="list-style-type: none"> • Any excavated or stockpile of dusty material should be covered entirely by impervious sheeting or sprayed with water to maintain the entire surface wet and then removed or backfilled or reinstated where practicable within 24 hours of the excavation or unloading; • Any dusty materials remaining after a stockpile is removed should be wetted with water and cleared from the surface of roads; • A stockpile of dusty material should not be extend beyond the pedestrian barriers, fencing or traffic cones; • The load of dusty materials on a vehicle leaving a construction site should be covered entirely by impervious sheeting to ensure that the dusty materials do not leak from the vehicle; • Where practicable, vehicle washing facilities with high pressure water jet should be provided at every discernible or designated vehicle exit point. The area where vehicle washing takes place and the road section between the washing facilities and the exit point should be paved with concrete, bituminous materials or hard cores; • When there are open excavation and reinstatement works, hoarding of not less than 2.4m high should be provided as far as practicable along the site boundary with provision for public crossing. Good site practice shall also be adopted by the Contractor to ensure the conditions of the hoardings are properly maintained throughout the construction period; 	Minimize dust impact at the nearby sensitive receivers	Contractor	All construction sites	Construction phase	APCO To control the dust impact to meet HKAQO and TM-EIAO

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the Measures?	Location of the measures	When to implement the Measures?	What requirements or standards for the measures to achieve?
		<ul style="list-style-type: none"> • The portion of any road leading only to construction site that is within 30m of a vehicle entrance or exit should be kept clear of dusty materials; • Surfaces where any pneumatic or power-driven drilling, cutting, polishing or other mechanical breaking operation takes place should be sprayed with water or a dust suppression chemical continuously; • Any area that involves demolition activities should be sprayed with water or a dust suppression chemical immediately prior to, during and immediately after the activities so as to maintain the entire surface wet; • Where a scaffolding is erected around the perimeter of a building under construction, effective dust screens, sheeting or netting should be provided to enclose the scaffolding from the ground floor level of the building, or a canopy should be provided from the first floor level up to the highest level of the scaffolding; • Any skip hoist for material transport should be totally enclosed by impervious sheeting; and • Every stock of more than 20 bags of cement or dry pulverized fuel ash (PFA) should be covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides. 					
Noise Impact (Construction Phase)							
S4.9	N1	Implement the following good site management practices: <ul style="list-style-type: none"> • only well-maintained plant should be operated on-site and plant should be serviced regularly during the construction programme; • machines and plant (such as trucks, cranes) that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum; • plant known to emit noise strongly in one direction, where possible, be orientated so that the noise is directed away from nearby NSRs; • silencers or mufflers on construction equipment should be properly fitted and maintained during the construction works; • mobile plant should be sited as far away from NSRs as possible and practicable; and • material stockpiles, mobile container site office and other structures should be effectively utilised, where practicable, to screen noise from on-site construction activities. 	Control construction airborne noise	Contractor	All construction sites	Construction phase	Annex 5, TM-EIAO
S4.9	N2	Install temporary site hoarding (approx. 2.4m high) located on the site boundaries between noisy construction activities and NSRs. The conditions of the hoardings shall be properly maintained throughout the construction period.	Reduce the construction noise levels at low-level	Contractor	All construction sites	Construction phase	Annex 5, TM-EIAO

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the Measures?	Location of the measures	When to implement the Measures?	What requirements or standards for the measures to achieve?
			zone of NSRs through partial screening.				
S4.9	N3	Install movable noise barriers, full enclosure and acoustic mat, screen the noisy plants including air compressor and generator.	Screen the noisy plant items to be used at all construction sites	Contractor	All construction sites	Construction phase	Annex 5, TM-EIAO
S4.9	N4	Use of "Quiet" Plant and Working Methods	Reduce the noise levels of plant items	Contractor	All construction sites	Construction phase	Annex 5, TM-EIAO
S4.9	N5	Sequencing operation of construction plants where practicable.	Operate sequentially within the same work site to reduce the construction airborne noise	Contractor	All construction sites	Construction phase	Annex 5, TM-EIAO
Water Quality Impact (Construction Phase)							
S5.7	W1	<p>Construction Runoff</p> <p>In accordance with the Practice Note for Professional Persons on Construction Site Drainage, Environmental Protection Department, 1994 (ProPECC PN 1/94), construction phase mitigation measures should be provided and the Storm Water Pollution Control Plan is given below.</p> <p>Storm Water Pollution Control Plan</p> <ul style="list-style-type: none"> At the start of site establishment, perimeter cut-off drains to direct off-site water around the site should be constructed with internal drainage works and erosion and sedimentation control facilities implemented. Channels (both temporary and permanent drainage pipes and culverts), earth bunds or sand bag barriers should be provided on site to direct stormwater to silt removal facilities. The design of the temporary on-site drainage system will be undertaken by the Contractor prior to the commencement of construction. Diversion of natural stormwater should be provided as far as possible. The design of temporary on-site drainage should prevent runoff going through site surface, construction machinery and equipment in order to avoid or minimize polluted runoff. Sedimentation tanks with sufficient capacity, constructed from pre-formed individual cells of approximately 6 to 8m³ capacities, are recommended as a general mitigation measure which can be used for settling surface runoff prior to disposal. The system capacity shall be flexible and able to handle multiple inputs from a variety of sources and suited to applications 	Control construction runoff	Contractor	All construction sites	Construction phase	WPCO, EIAO, TM-EIAO

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the Measures?	Location of the measures	When to implement the Measures?	What requirements or standards for the measures to achieve?
		<p>where the influent is pumped.</p> <ul style="list-style-type: none"> • The dikes or embankments for flood protection should be implemented around the boundaries of earthwork areas. Temporary ditches should be provided to facilitate the runoff discharge into an appropriate watercourse, through a silt/sediment trap. The silt/sediment traps should be incorporated in the permanent drainage channels to enhance deposition rates. • The design of efficient silt removal facilities should be based on the guidelines in Appendix A1 of ProPECC PN 1/94. The detailed design of the sand/silt traps should be undertaken by the Contractor prior to the commencement of construction. • Construction works should be programmed to minimize surface excavation works during the rainy seasons (April to September). All exposed earth areas should be completed and vegetated as soon as possible after earthworks have been completed. If excavation of soil cannot be avoided during the rainy season, or at any time of year when rainstorms are likely, exposed slope surfaces should be covered by tarpaulin or other means. • All drainage facilities and erosion and sediment control structures should be regularly inspected and maintained to ensure proper and efficient operation at all times and particularly following rainstorms. Deposited silt and grit should be removed regularly and disposed of by spreading evenly over stable, vegetated areas. • Measures should be taken to minimize the ingress of site drainage into excavations. If the excavation of trenches in wet periods is necessary, it should be dug and backfilled in short sections wherever practicable. Water pumped out from trenches or foundation excavations should be discharged into storm drains via silt removal facilities. • All open stockpiles of construction materials (for example, aggregates, sand and fill material) of more than 50m³ should be covered with tarpaulin or similar fabric during rainstorms. Measures should be taken to prevent the washing away of construction materials, soil, silt or debris into any drainage system. • Manholes (including newly constructed ones) should always be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris being washed into the drainage system and storm runoff being directed into foul sewers. • Precautions be taken at any time of year when rainstorms are likely, actions to be taken when a rainstorm is imminent or forecasted, and actions to be taken during or after rainstorms are summarised in Appendix A2 of ProPECC PN 1/94. Particular attention should be paid to the control of silty surface runoff 					

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the Measures?	Location of the measures	When to implement the Measures?	What requirements or standards for the measures to achieve?
		<p>during storm events.</p> <ul style="list-style-type: none"> All vehicles and plant should be cleaned before leaving a construction site to ensure no earth, mud, debris and the like is deposited by them on roads. An adequately designed and sited wheel washing facilities should be provided at every construction site exit where practicable. Wash-water should have sand and silt settled out and removed at least on a weekly basis to ensure the continued efficiency of the process. The section of access road leading to, and exiting from, the wheel wash bay to the public road should be paved with sufficient backfall toward the wheel-wash bay to prevent vehicle tracking of soil and silty water to public roads and drains. Oil interceptors should be provided in the drainage system downstream of any oil/fuel pollution sources. The oil interceptors should be emptied and cleaned regularly to prevent the release of oil and grease into the storm water drainage system after accidental spillage. A bypass should be provided for the oil interceptors to prevent flushing during heavy rain. Construction solid waste, debris and rubbish on site should be collected, handled and disposed of properly to avoid water quality impacts. All fuel tanks and storage areas should be provided with locks and sited on sealed areas, within bunds of a capacity equal to 110% of the storage capacity of the largest tank to prevent spilled fuel oils from reaching water sensitive receivers nearby. Regular environmental audit on the construction site should be carried out in order to prevent any malpractices. Notices should be posted at conspicuous locations to remind the workers not to discharge any sewage or wastewater into the meander, wetlands and fish ponds. 					
S5.7	W2	<p>Sewage from Workforce</p> <ul style="list-style-type: none"> Portable chemical toilets and sewage holding tanks should be provided for handling the construction sewage generated by the workforce. A licensed Contractor should be employed to provide appropriate and adequate portable toilets and be responsible for appropriate disposal and maintenance. Notices should be posted at conspicuous locations to remind the workers not to discharge any sewage or wastewater into the nearby environment during the construction phase of the Project. Regular environmental audit on the construction site should be conducted in order to provide an effective control of any malpractices and achieve continual improvement of environmental performance on site. It is anticipated that sewage generation during the construction phase of the Project would not cause water quality impact after undertaking all required measures. 	Handling of site sewage	Contractor	All construction sites	Construction phase	WPCO, EIAO, TM-EIAO

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the Measures?	Location of the measures	When to implement the Measures?	What requirements or standards for the measures to achieve?
Waste Management (Construction Waste)							
S7.6	WM1	<p>Waste Reduction Measures</p> <p>Waste reduction is best achieved at the planning and design phase, as well as by ensuring the implementation of good site practices. The following recommendations are proposed to achieve reduction:</p> <ul style="list-style-type: none"> • segregate and store different types of waste in different containers, skip or stockpiles to enhance reuse or recycling of materials and their proper disposal; • proper storage and site practices to minimize the potential for damage and contamination of construction materials; • plan and stock construction materials carefully to minimize amount of waste generated and avoid unnecessary generation of waste; • sort out demolition debris and excavated materials from demolition works to recover reusable/recyclable portions (i.e. soil, broken concrete, metal etc.); and • provide training to workers on the importance of appropriate waste management procedures, including waste reduction, reuse and recycling. 	Reduce waste generation	Contractor	All construction sites where practicable	Prior to the commencement of construction	Waste Disposal Ordinance
S7.6	WM2	Prepare Waste Management Plan and submit to the Engineer for approval	Minimize waste generation during construction	Contractor	All construction sites	Construction phase	Waste Disposal Ordinance
S7.6	WM3	<p>Good Site Practice</p> <p>The following good site practices are recommended throughout the construction activities:</p> <ul style="list-style-type: none"> • nomination of an approved personnel, such as a site manager, to be responsible for the implementation of good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site; • training of site personnel in site cleanliness, appropriate waste management procedures and concepts of waste reduction, reuse and recycling; • provision of sufficient waste disposal points and regular collection for disposal; • appropriate measures to minimize windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers; • regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors; 	Minimize waste generation during construction	Contractor	All construction sites	Construction phase	Waste Disposal Ordinance
S7.6	WM4	<p>Storage of Waste</p> <p>The following recommendation should be implemented to minimize the impacts:</p>	Minimize waste from storage impacts	Contractor	All construction	Construction phase	Waste Disposal Ordinance

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the Measures?	Location of the measures	When to implement the Measures?	What requirements or standards for the measures to achieve?
		<ul style="list-style-type: none"> waste such as soil should be handled and stored well to ensure secure containment; stockpiling area should be provided with covers and water spraying system to prevent materials from wind-blown or being washed away; different locations should be designated to stockpile each material to enhance reuse; 			sites		
S7.6	WM5	<p>Collection and Transportation of Waste</p> <p>The following recommendation should minimize the impacts:</p> <ul style="list-style-type: none"> remove waste in timely manner; employ the trucks with cover or enclosed containers for waste transportation; obtain relevant waste disposal permits from the appropriate authorities; and disposal of waste should be done at licensed waste disposal facilities. 	Minimize waste from storage impacts	Contractor	All construction sites	Construction phase	Waste Disposal Ordinance
S7.6	WM6	<p>Excavated and C&D Material</p> <p>Wherever practicable, C&D materials should be segregated from other wastes to avoid contamination and ensure acceptability at public filling areas or reclamation sites. The following mitigation measures should be implemented in handling the excavated and C&D materials:</p> <ul style="list-style-type: none"> maintain temporary stockpiles and reuse excavated fill material for backfilling; carry out on-site sorting; deliver surplus artificial hard materials to Tuen Mun Area 38 recycling plant or its successor for recycling into subsequent useful products; make provisions in the Contract documents to allow and promote the use of recycled aggregates where appropriate; implement a recording system for the amount of waste generated, recycled and disposed of for checking; <p>Standard formwork should be used as far as practicable in order to minimize the arising of C&D waste. The use of more durable formwork (e.g. metal hoarding) or plastic facing should be encouraged in order to enhance the possibility of recycling. The purchasing of construction materials should be carefully planned in order to avoid over ordering and wastage. Wheel wash facilities have to be provided at the site entrance before the trucks leaving the works area.</p>	Minimize waste impacts from excavated and C&D materials	Contractor	All construction sites	Construction phase	<ul style="list-style-type: none"> Land (Miscellaneous Provisions) Ordinance Waste Disposal Ordinance ETWB TCW No. 19/2005
S7.6	WM8	<p>Chemical Waste</p> <ul style="list-style-type: none"> If chemical wastes are produced at the construction site, the Contractors should register with EPD as chemical waste producers. Chemical wastes should be stored in appropriate containers and collected by a licensed chemical waste Contractor. Chemical wastes (e.g. spent lubricant oil) should be recycled at an appropriate facility as far as possible, while the chemical 	Control the chemical waste and ensure proper storage, handling and disposal.	Contractor	All construction sites	Construction phase	<ul style="list-style-type: none"> Waste Disposal (Chemical Waste General) Regulation Code of Practice on the Packaging, Labelling and

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the Measures?	Location of the measures	When to implement the Measures?	What requirements or standards for the measures to achieve?
		waste that cannot be recycled should be disposed of at either the Chemical Waste Treatment Centre, or another licensed facility, in accordance with the Waste Disposal (Chemical Waste) (General) Regulation.					Storage of Chemical Waste
S7.6	WM9	General Waste <ul style="list-style-type: none"> General refuse should be stored in enclosed bins separately from construction and chemical wastes. Recycling bins should also be placed to encourage recycling. Preferably enclosed and covered areas should be provided for general refuse collection and routine cleaning for these areas should also be implemented to keep areas clean. A reputable waste collector should be employed to remove general refuse on a daily basis. 	Minimize production of the general refuse and avoid odour, pest and litter impacts	Contractor	All construction sites	Construction phase	<ul style="list-style-type: none"> Waste Disposal Ordinance
S7.6	WM10	Sewage <ul style="list-style-type: none"> The WMP should document the locations and number of portable chemical toilets depending on the number of workers, land availability, site condition and activities. Regularly collection by licensed collectors should be arranged to minimize potential environmental impacts. 	Minimize production of sewage impacts	Contractor	All construction sites	Construction phase	<ul style="list-style-type: none"> Waste Disposal Ordinance
S7.6	WM11	Topsoil reuse – Topsoil, where identified, should be stripped and stored for re-use in the construction of the soft landscape works, where practical. This is considered a general measure for good site practice.	Good site practice	Contractor / Project Proponent	Onsite	Construction Phase	<ul style="list-style-type: none"> ETWB Technical Circular (Works) No.29/2004
Landscape and Visual (Construction)							
S.12.9 MM3	LV5	Open Space Provision - the principles adopted in the RODP planning ensure that public open space systems are incorporated. All requirements for open space areas stipulated in the planning documents for the formulation of the Preliminary Layout Plan should be adhered to.	Reprovision of open space. Enhance visual amenity of the area and improve the overall landscape character	Government Developer / Detailed Design Consultant / Contractor	Onsite as stipulated in the planning documents for the formulation of the Preliminary Layout Plan	Prior to Construction and Construction Phase	Hong Kong Planning Standards and Guidelines (HKPSG) issued by the Planning Department (As at Aug 2011); Sustainable Building Design Guidelines
S.12.9 MM4	LV6	Tree Protection & Preservation – Existing trees to be retained within the Project Site should be carefully protected during construction. In particular OVTs will be preserved according to ETWB Technical Circular (Works) No. 29/2004. Detailed Tree Protection Specification shall be provided in the Contract Specification. Under this specification, the Contractor shall be required to submit, for approval, a detailed working method statement for the protection of trees prior to	Protect and Preserve Trees	Government Developer / Detailed Design Consultant / Contractor	Onsite as stipulated in the planning documents for the formulation of	Prior to Construction and Construction Phase	ETWB Technical Circular Works (TCW) No. 29/2004 and 3/2006

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the Measures?	Location of the measures	When to implement the Measures?	What requirements or standards for the measures to achieve?
		<p>undertaking any works adjacent to all retained trees, including trees in Contractor's works areas.</p> <p>A detailed tree survey will be carried out for the Tree Removal Application (TRA) process which will be carried out at the later detailed design stage of the Project. The detailed tree survey will propose which trees should be retained, transplanted or felled and will include details of tree protection measures for those trees to be retained.</p>			the Preliminary Layout Plan		
S.12.9 MM5	LV7	<p>Tree Transplantation – Trees unavoidably affected by the Project works should be transplanted where practical. Trees should be transplanted straight to their final receptor site and not held in a temporary nursery as far as possible. A detailed Tree Transplanting Specification shall be provided in the Contract Specification, where applicable. Sufficient time for necessary tree root and crown preparation periods shall be allowed in the project programme.</p> <p>A detailed transplanting proposal will be submitted to relevant government departments for approval in accordance with ETWBTC 2/2004 and 3/2006 and final locations of transplanted trees should be agreed prior to commencement of the work.</p> <p>For trees associated with highways e.g. roadside planting along highways, that are unavoidably affected and should be transplanted, HyD HQ/GN/13 'Interim Guidelines for Tree Transplanting Works under Highways Department's Vegetation Maintenance Ambit' should be referred to.</p>	Transplant Trees where suitable for transplantation	Government Developer / Detailed Design Consultant / Contractor	Onsite where possible. Otherwise consider offsite locations	Prior to Construction, Construction Phase & Maintenance in Operation Phase	ETWB TCW 3/2006 and 2/2004 HyD HQ/GN/13 Interim Guidelines for Tree Transplanting Works under Highways Department's Vegetation Maintenance Ambit
S.12.9 MM7	LV9	<p>Compensatory Planting – Compensatory tree planting for felled trees shall be provided to the satisfaction of relevant Government departments. Required numbers and locations of compensatory trees shall be determined and agreed separately with Government during the Tree Removal Application process under ETWBTC 3/2006.</p> <p>Compensatory planting is proposed at the potential open areas such as open spaces, amenity areas, open areas of the streetscapes, as well as the open areas within development lots.</p> <p>Compensatory planting for shrubs should be considered in suitable locations. Native species such as <i>Melastoma malabathricum</i>, <i>Diospyros vaccinioides</i>, <i>Gardenia jasminoides</i>, <i>Ixora chinensis</i>, <i>Ligustrum sinense</i>, <i>Litsea rotundifolia</i>, <i>Melastoma dodecandrum</i>, <i>Atalantia buxifolia</i>, <i>Rhodomyrtus tomentosa</i>, <i>Rhaphiolepis indica</i>, and <i>Rhododendron simsii</i> are suggested.</p>	Compensate for trees and shrubs lost due to the Project.	Government Developer / Detailed Design Consultant / Contractor	Onsite where possible. Otherwise consider offsite locations	Prior to Construction, Construction Phase & Maintenance in Operation Phase	ETWB TCW 3/2006 and 2/2004
S.12.9 MM9	LV11	Vertical Greening – Planting of climbers to grow up vertical surfaces were appropriate (e.g. building edges, piers).	Soften hard surfaces and	Project Proponent /	On appropriate	Prior to Construction,	ETWB TCW No. 11/2004 – Cyber

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the Measures?	Location of the measures	When to implement the Measures?	What requirements or standards for the measures to achieve?
			facilities	Detailed Design Consultant / Contractor / Maintenance Authority	structures	Construction Phase & Maintenance in Operation Phase	Manual for Greening
S.12.9 MM10	LV12	Green Roof – Roof greening where appropriate should be established on proposed buildings as per the guidelines stated. These guidelines provide further details including information regarding structural loading, design, maintenance, etc. considerations as well as providing information on what types of plants might be suitable.	Reduce exposure to untreated concrete surfaces and particularly mitigate visual impact to VSRs at high levels. Provide greening.	Project Proponent / Detailed Design Consultant / Contractor / Maintenance Authority	On appropriate buildings	Prior to Construction, Construction Phase & Maintenance in Operation Phase	CIBSE HK Branch, Technical Guidelines for Green Roof Systems in Hong Kong (2011); ArchSD/Urbis Study on Green Roof Application in HK (2007)
S.12.9 MM11	LV13	Screen Planting – Tall screen/buffer trees and shrubs should be planted. This measure may additionally form part of the compensatory planting.	To screen proposed structures such as roads and buildings. Improve compatibility with the surrounding environment and create a pleasant pedestrian environment	Government / Developer / Detailed Design Consultant / Contractor	Along roads, around suitable built structures, or around VSRs to contain their view out to the NDA Maintenance and create a pleasant Contractor structures	Prior to Construction, Construction Phase & Maintenance in Operation Phase	ETWBTC 3/2006
S12.9 MM14.5	LV20	Screen Hoarding – Screen hoarding shall be erected along areas of the construction works site boundary where the works site borders publically accessible routes and/or is close to visually sensitive receivers (VSRs). It is proposed that the screening be compatible with the surrounding environment and where possible, nonreflective, recessive colours be used. Any works areas near the ecological sensitive areas should erect 2m high dull green site boundary fence. Details can refer to the ecological impact assessment (Chapter 13 of the EIA report).	To screen undesirable views of the works site.	Contractor	Throughout NDAs	Construction Phase	
S12.9	LV21	Light Control – Construction day and night time lighting should be controlled to	To minimize glare	Government /	Throughout	Construction	

EIA Ref.	EM&A Log Ref	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the Measures?	Location of the measures	When to implement the Measures?	What requirements or standards for the measures to achieve?
MM14.6		<p>minimize glare impact to adjacent VSRs during the Construction phase.</p> <p>Street and night time lighting shall also be controlled to minimize glare impact to adjacent VSRs during the operation phase.</p>	impact to adjacent VSRs	Developer / Contractor	NDAs	and Operation Phases	
Ecology (Construction Phase)							
S.13.9	E13	<p>Review design and construction methods for bridges, especially those on the Sheung Yue and tidal Ng Tung Rivers, and adopt measures which minimize impacts on rivers and disturbance and fragmentation impacts on fauna.</p> <p>No construction during ardeid breeding season (1 March to 31 July) along Sheung Yue River north and east of KTN area D1-5 and east of D1-9 and C2-3 and restriction of working hours on new pedestrian bridges over the Sheung Yue River and tidal Ng Tung River to 09.00 to 17.30 during the ardeid breeding season (1 March to 31 July).</p> <p>Provision of alternative foraging habitat along main river channels for large waterbirds.</p>	Minimize impacts on rivers and disturbance and fragmentation impacts on fauna.	Project Proponent / Detailed Design Consultant / Contractor	Along and within the Sheung Yue, Ng Tung and Shek Sheung Rivers	Detailed design and construction phases.	TM-EIAO.
S.13.9	E16	<p>Creation of Green Corridors along the Sheung Yue, Ng Tung and Shek Sheung Rivers, retention and provision of screen plantings where feasible; provision of Open Space areas and development areas along river corridors;</p> <p>Design and erection of 2m high solid dull green site barrier fence between river channel and any active works area along or adjacent to Ng Tung, Sheung Yue and Shek Sheung Rivers.</p> <p>Ng Tung, Sheung Yue and Shek Sheung Rivers screen planting.</p>	Minimize disturbance to waterbirds using Ng Tung, Sheung Yue and Shek Sheung River channels.	Detailed Design Consultant / Contractor	Ng Tung, Sheung Yue and Shek Sheung Rivers	Detailed design and construction phases.	TM-EIAO.
S.13.9	E19	<p>Use opaque, non-transparent, non-reflective noise barriers for all construction sites.</p> <p>Unnecessary lighting should be avoided.</p>	Minimize mortality impacts on birds.	Contractor	All construction sites	Construction phase.	TM-EIAO.
